


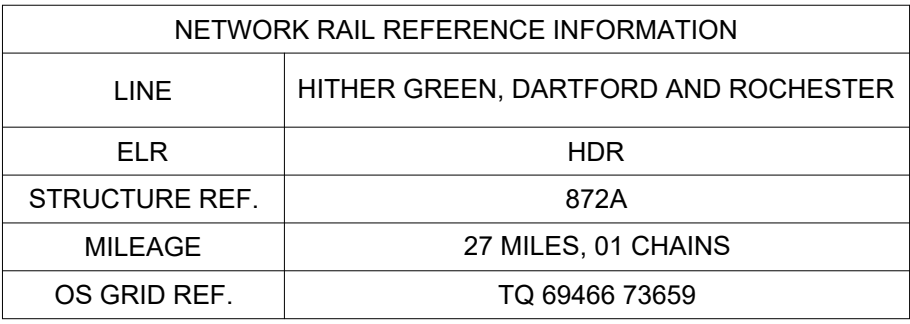

"SITE COMPOUND LOCATION TO
BE AGREED AT FORM B STAGE"

CRANE SHOWN
INDICATIVELY

W 3 FARM ROAD

9

CONSTRUCTION SEQUENCE

STAGE 1
PREPARE SITE FOR CONSTRUCTION.
ERECT TEMPORARY FENCING, LAY-DOWN AREA, MESS FACILITIES ETC.
CLEAR VEGETATION, REMOVE OBSTACLES, NWR BOUNDARY FENCES
ETC.
LOCATE AND MARK SERVICES (SERVICES TO BE PROTECTED DURING
CONSTRUCTION PERIOD)
CREATE TEMPORARY WALKWAYS, CRANE/PILING MATS, SIGNAGE ETC.

STAGE 2
INSTALL PILES FOR BRIDGE/STAIRCASE SUPPORTS (ALO WORKING
ARRANGEMENTS0.
NB : TEMPORARY SUPPORTS FOR THESE STRUCTURES TO BE
CONSIDERED AT DETAILED DESIGN STAGE

STAGE 3
CONSTRUCT NEW PERMANENT PATHWAYS CONNECTING TO EXISTING
PUBLIC HIGHWAYS

STAGE 4

INSTALL THE LANDING TRESTLES (ALO WORKING ARRANGEMENTS)


STAGE 5
INSTALL BRIDGE DECK AND STAIRCASES DURING SINGLE EXTENDED
POSSESSION (TBC)

STAGE 6
WHEN ERECTION OF BRIDGE AND STAIRS IS COMPLETE , INFILL PLATES
TO BE INSTALLED AT LIFTING POINTS.
ALL JOINTS TO BE SEALED, AND FINALLY ALL
WATERPROOFING/SURFACING TO BE MADE GOOD AT JOINTS AND LIFTING
POINT POSITIONS AS NECESSARY.

STAGE 7
INSTALL NEW SIGNAGE AND PERMANENT FENCES/GATES

STAGE 8

DEMOBILISE FROM SITE AND HANDOVER



TO BE REPRODUCED IN COLOUR

A03	21/10/22	FORM A ISSUE			
A02	29/09/22	FORM A ISSUE	JS	NM	DG
A01	12/09/22	PRE-IDR ISSUE	NM	IH	DG
Rev	Date	Description of Revisions	Drawn	Chkd	Appr
Status					

FOR ACCEPTANCE



Contractor(s)



Brunel House
RTC Business Park
London Road
Derby DE24 8UP

Tel: +44 (0)784 282 6635
Fax: +44 (0)784 282 6635

Project

SHORNEMEAD LX FOOTBRIDGE

Drawing Title

TEMPORARY WORKS PLAN AND CONSTRUCTION SEQUENCE

Designed	N.MARSHALL	Signed	Date 21/10/22
Drawn	N. MARSHALL	Signed	Date 21/10/22
Checked	I. HILL	Signed	Date 21/10/22
Approved	D. GENT	Signed	Date 21/10/22

Scale(s)	1:500	ELR & Mileage	HDR 27m 01 CH
Alternative Reference	N/A	Sheet	1 of 1
Drawing Number	S2021-137-DRG-CIV-102		Revision A03
