


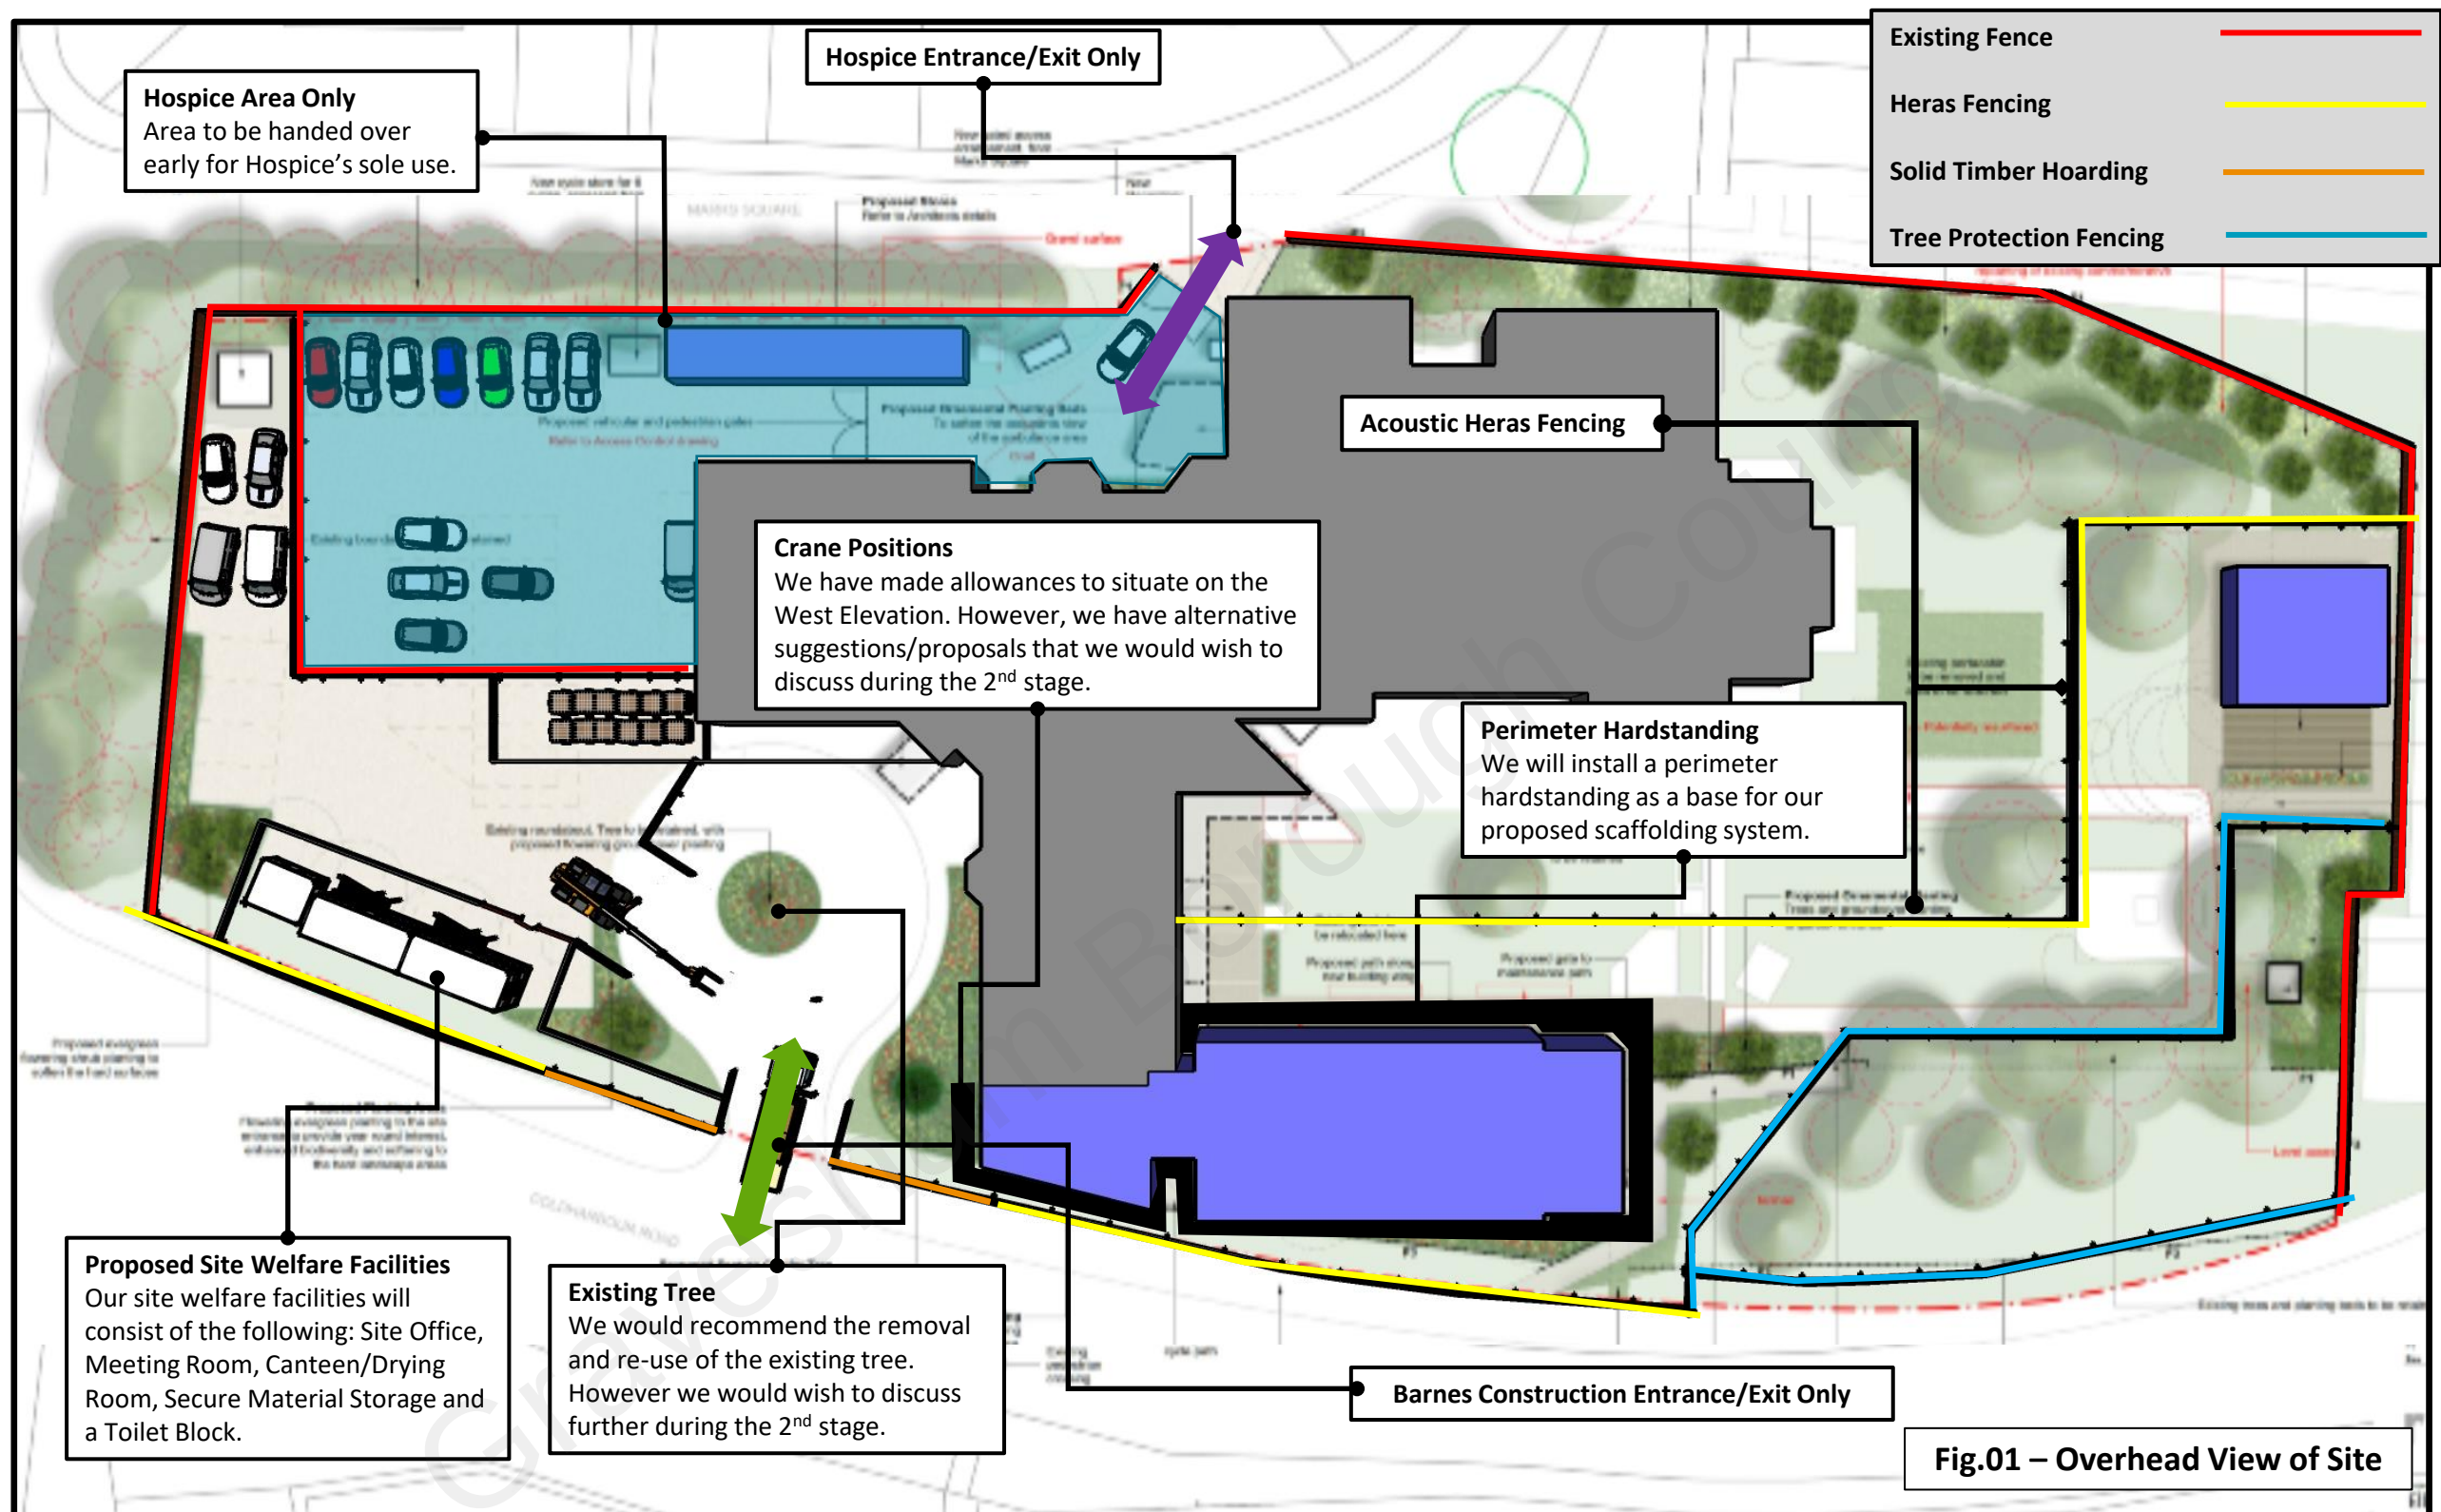

Routing of Delivery Vehicles

All delivery vehicles will enter the site via the Barnes Construction site entrance, as indicated. They will be met by our Banksman who will then advise of and assist all movements within the site. Vehicles will then turn on-site before existing via the same gate onto Coldharbour Road.

Parking & Turning Areas for Construction Traffic & Timing of Deliveries

As indicated, we have made a small allowance for our site management team to park their vehicles on the main site. Deliveries will also be timed sensitively to avoid busy periods. Drivers will be required to call ahead so that our Banksman can make provisions for their arrival to minimise disruption as far as possible.

Type & Location of Wheel Washing & Chassis Cleaning Facilities

Our logistics proposal ensures that vehicles will mostly be able to remain on hardstanding for the majority of their time on-site. During the groundworks stage, our subcontractor will be responsible for inspecting vehicle as they leave the site and ensuring appropriate wheel wash measures are in place if required.

Ellenor Hospice, Gravesend

Site Logistics Proposal

BC1953/SLP/001 Rev.B

ellenor.
hospice care in your home or ours

Barnes
CONSTRUCTION



Fig.02 – Main Site Compound

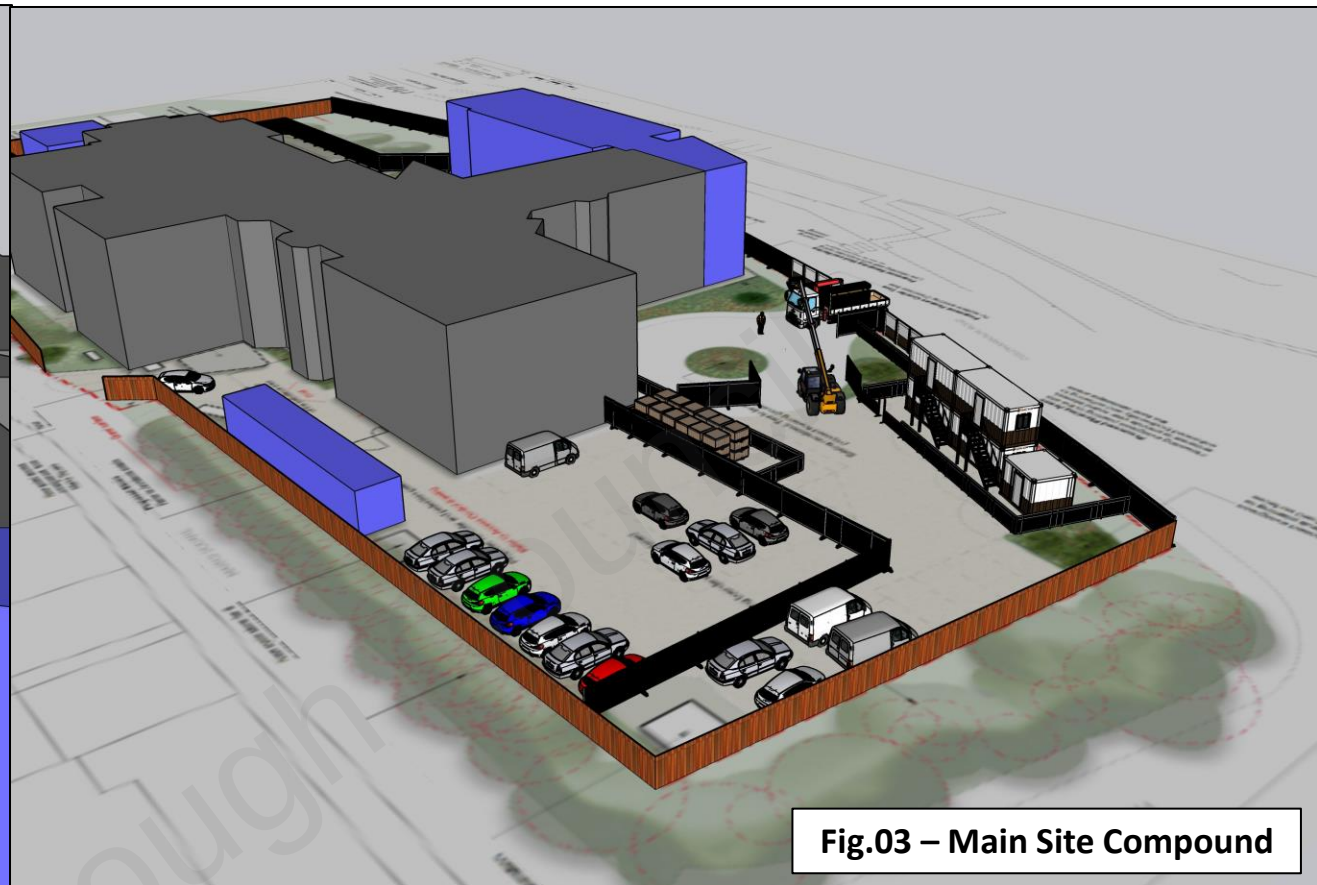


Fig.03 – Main Site Compound



Fig.04 – Existing Site Entrance



Fig.05 – Existing Pedestrian Crossing



Fig.06 – Existing Main Site Compound

Ellenor Hospice, Gravesend

Site Logistics Proposal

BCE4793/SLP/002 Rev.A

ellenor.
hospice care in your home or ours

Barnes
CONSTRUCTION
