

Tree Survey, Arboricultural Impact Assessment, Arboricultural Method Statement

for

Cold Harbour Road Gravesend

On behalf of

Frontier Estates

September 2022

Status: Planning

The Landscape Partnership Ltd is a practice of Chartered Landscape Architects, Chartered Ecologists and Chartered Environmentalists, registered with the Landscape Institute and a member of the Institute of Environmental Management & Assessment & the Arboricultural Association
The Landscape Partnership Limited
Registered Office:
Greenwood House
15a St Cuthberts Street
Bedford
MK40 3JG
01234 261315
Registered in England No 2709001

Contents

1	Introduction
2	Site Description
3	Survey Methodology
4	The Trees
5	Arboricultural Impact Assessment
6	Impact of Proposed Development on Retained Trees
7	Arboricultural Method Statement Methodology
8	Site Preparation/Demolition and Construction Close to Retained Trees
9	Services
10	Tree Protection Barrier
11	Conclusions
12	Recommendations
13	Project Contact Details

Appendices

1	BS 5837 Table 1
2	Tree Survey Schedule
3	Tree Preservation Order

Accompanying Drawings

1	TS Drawing B22032-TLP-601
2	AIA AMS Drawing B22032-TLP-602

1 Introduction

- 1.1 The Landscape Partnership has been commissioned by Frontier Estates to out a tree survey at Cold Harbour Road, Gravesend.
- 1.3 The site is not within a Conservation Area. A request was made to Gravesham Borough Council regarding whether any Tree Preservation Orders (TPO) covered the development Site. The Borough Council returned information relating to 'Land surrounding the Battle of Britain P.H., New House Lane, Northfleet', which indicated that the Copper Beech tree located within the western corner of the site was listed as protected by a TPO dated 14th July 1994. A copy of the TPO has been included within the appendices of this report. It has been noted and clarified by the Council that the TPO location map included within the TPO shows the location of the protected tree incorrectly, and that the map incorrectly shows an additional protected tree (lime). This additional tree is not present on site, and is not included in the 'First Schedule' listed within the TPO.
- 1.4 The site visit was carried out by Michael Roseveare in May 2022.

2 Site Description

- 2.1 The site is a former public house and associated car park and gardens. The site has been cleared and is now vacant except for some of the former car park and a few scattered landscape features including trees and hedges. There are few trees within the site boundary, and these are located to the western and the south-eastern boundaries and the north-eastern boundary with the neighbouring school.

3 Survey Methodology

- 3.1 The majority of the trees were surveyed with the benefit of a topographical survey. Where the location of a tree coincides with that shown on the TPO plan on the council's website the TPO number has been added for reference.
- 3.2 The trees were inspected from ground level and measurements taking in accordance with the recommendations set out in the British Standard 5837:2012. Canopy spreads have been measured and plotted to the 4 compass points (north, south, east and west).
- 3.3 The location of the surveyed trees is shown on the accompanying Tree Survey Plans numbered B22032-601. Where access was not possible measurements have been estimated. The surveyed trees are colour coded on the accompanying tree survey drawing according to their relevant BS category as follows:
 - A High quality and value (shown green)
 - B Moderate quality and value (shown blue)
 - C Low quality and value (shown grey)
 - U Unsuitable for retention (shown red)
- 3.4 The trees are also placed into sub categories 1, 2 and 3 according to the criteria in Table 1 in BS 5837:2012 (see Appendix 1).
- 3.5 The tree data collected is used to enable the current canopy spread of the surveyed trees and Root Protection Area (RPA) to be plotted on a drawing. The RPA is defined in accordance with the recommendations set out in section 4.6 of BS 5837:2012.
- 3.6 The calculated RPA should be capped at 707m², which is equivalent to a circle with a radius of 15m or a square with approximately 26m sides.
- 3.7 The RPA may be refined, by considering current on-site constraints to root activity such as buildings, earthworks and hard paving. This forms part of the design process for the proposed development.

- 3.8 The site survey also provides a schedule of recommendations for tree surgery works where appropriate.

4 The Trees

- 4.1 The trees fall into several character groups as described below.

Character group one: includes the two mature trees growing within the Site in the roadside verge close to the junction with New House Lane. These trees are substantial and provide a significant amenity locally.

Character group two: includes the several trees along the site south-eastern boundary including a maturing Bay tree within the adjacent domestic garden. They provide some amenity to the site and its neighbour but are relatively small and in the case of the Goat Willow have a relatively short useful life expectancy unless coppiced, which will reduce its stature periodically. If retained in its current form it will collapse in the next 5 years as growth of its crown exposes the relatively poor structure of its natural form.

Character Group three: Includes the trees and hedge along the sites boundary with the school. Largely scrub in nature the hedge provides a screen to the school. It is of relatively low quality and is likely to develop and decline over several cycles. Adding new trees to the edge of the group will improve the nature of the amenity that it provides.

Character group four: includes the Elm group adjacent to New House Lane. This group of trees includes a mix of dead and relatively young vigorous trees. The cycle of growth and dieback will be repeated unless the group is treated as coppice.

5 Arboricultural Impact Assessment (AIA)

- 5.1 The AIA uses information provided in the tree survey to identify areas where the proposed development construction may be at odds with accepted standards in terms of a tree's requirements for soil volume in which to maintain existing roots and shoots and soil volume for future growth.
- 5.2 Details of the trees surveyed are given in the accompanying Tree Survey Schedule. Tree locations are shown on the accompanying Tree Survey Drawing B22032-TLP-601.
- 5.3 The quality and relative importance of each is shown as coloured polygons. The colour used relates to the British Standard categories as follows: A, green; B, blue; C, grey and U, red (see drawing B22032-TLP-601). Red trees are discounted as they are recommended for removal. In general, the design process will try to retain A and B category trees. Proposed construction will therefore normally be excluded from the root protection area of A and B category trees.
- 5.4 The AIA considers existing site conditions and the effect that they may have on the development of the surveyed trees' root systems. Hard structures such as buildings and paved roads and paths can influence the root activity of trees by reducing the availability of both moisture and nutrients.

6 Impact of Proposed Development on Retained Trees

- 6.1 Refer to the accompanying AIA AMS drawing B22032-TLP-602 for the relationship between the proposed development and the trees on the site.
- 6.2 The proposed redevelopment of the site includes the construction of a care home and associated infrastructure including access, car parking and landscape grounds.
- 6.3 The following trees and a hedge will be removed to enable the proposed development:

G3 dead and dying Elm	To enable the proposed access
-----------------------	-------------------------------

G8 Privet	To enable the proposed access and parking
-----------	---

6.4 The following trees may be affected by the proposed development:

T1 Beech (TPO)	Construction of a proposed path and boundary railings
T2 Pear	Construction of a proposed path
T9 Silver Birch	Construction of a proposed path
T10 Goat Willow	Construction of a proposed path and utilities, coppice to enable retention and avoid the collapse of the trees crown

7 Arboricultural Method Statement Methodology

- 7.1 The arboricultural method statement provides the means by which areas of construction activity or working space requirements identified in the AIA as being within or close to the RPA of retained trees, can be achieved whilst minimising the impact of that construction activity on the affected trees.
- 7.2 The excavation of foundations for buildings and hard surfaces on sites where trees are present may result in root damage and removal. Where root loss is likely to occur, it is important that a method of construction that minimises the impact on tree roots is used.

8 Site Preparation/Demolition and Construction Close to Retained Trees

- 8.2 All site preparation work including soil striping should be carried out after the tree protection barriers have been erected. Pruning work on T10 should be carried out at an early stage of the development to ensure that the proposed path can be constructed.
- 8.3 Damage to retained tree roots is to be avoided during all building activity on the site.
- 8.4 The two sections of path within the root protection areas of T1, T2, T9 and T10 identified above and shown on the drawing B22032-TLP-602 will be constructed using the "no dig" principles set out in Arboricultural Association guidance note 12 which is appended to this report. T10, a multi stemmed Goat Willow will be coppiced prior to the construction work being carried out. The pruning work is considered necessary because of the size of the trees crown and the likelihood of crown of the tree to collapse due to its size.
- 8.5 All excavation associated with the construction of the proposed boundary railings within the root protection areas of retained trees T1 and T2 will be carried out by hand. The design will allow local amendment to the location of each post hole should tree roots be encountered so that the removal of tree roots which are greater than 25mm in diameter can be avoided. The concrete required to support each railing supporting post will be contained within each post hole by lining the hole with polyethene DPC materials to prevent concrete liquor leaching into the soil and cause tree root damage.

9 Services

- 9.1 All service runs are to be placed outside the RPA of trees on and adjacent to the site. Where it is not possible to achieve this, the section of service run which passes within the RPA of a tree will be hand dug in accordance with 'broken trenches' (NJUG 4 section 4, appendix 13.4). This will ensure that tree roots are not damaged during the installation of the service. All root pruning will be agreed be-forehand with the named arboriculturist in consultation with the local authority arboricultural officer. All root pruning will be in accordance with BS 3998: 2010. All routes for overhead services

will aim to avoid the trees. Where this is unavoidable any tree work will be agreed prior to commencement with the Council's Arboricultural Officer.

10 Tree Protection Barrier

- 10.1 Trees retained in close proximity to the construction area of the site will be protected by the erection of a tree protection barrier in the location shown on the accompanying AIA AMS Plan Number B22032-TLP-602. The tree protection barrier will be erected prior to any other work on the development starting and will remain in situ until the construction process has been completed.

11 Conclusions

- 11.1 The tree survey includes trees of varying ages and condition. The most significant surveyed trees lie along the boundary of the site, with Tree T1 Copper Beech (protected by a TPO) lying within the site but beyond the proposed Care Home boundary railing, and will be largely unaffected by the proposed care home development. There is a minor incursion into the root protection areas of trees T1 and T2 where the car park for the now demolished public house is located. The incursion will have a minor impact on the trees which will be mitigated by using a "no dig" form of construction.

12 Recommendations

- 12.1 This report should be read in conjunction with the tree survey drawing B22032-TLP-601 and AIA AMS drawing B22032-TLP-602.

13 Project Contact Details

Client:	Frontier Estates
Arboriculturist:	Michael Roseveare, The Landscape Partnership Tel: 01394 380509
Local Planning Authority:	Gravesham Borough Council

Table 1 Cascade chart for tree quality assessment

Category and definition	Criteria (including subcategories where appropriate)	Identification on plan
Trees unsuitable for retention (see Note)		
Category U Those in such a condition that they cannot realistically be retained as living trees in the context of the current land use for longer than 10 years	- Trees that have a serious, irremediable, structural defect, such that their early loss is expected due to collapse, including those that will become unviable after removal of other category U trees (e.g. where, for whatever reason, the loss of companion shelter cannot be mitigated by pruning) - Trees that are dead or are showing signs of significant, immediate, and irreversible overall decline - Trees infected with pathogens of significance to the health and/or safety of other trees nearby, or very low quality trees suppressing adjacent trees of better quality <i>NOTE</i> Category U trees can have existing or potential conservation value which it might be desirable to preserve; see 4.5.7.	See Table 2
1 Mainly arboricultural qualities 2 Mainly landscape qualities 3 Mainly cultural values, including conservation		
Trees to be considered for retention		
Category A Trees of high quality with an estimated remaining life expectancy of at least 40 years	Trees that are particularly good examples of their species, especially if rare or unusual; or those that are essential components of groups or formal or semi-formal arboricultural features (e.g. the dominant and/or principal trees within an avenue)	Trees, groups or woodlands of significant conservation, historical, commemorative or other value (e.g. veteran trees or wood-pasture)
Category B Trees of moderate quality with an estimated remaining life expectancy of at least 20 years	Trees that might be included in category A, but are downgraded because of impaired condition (e.g. presence of significant though remediable defects, including unsympathetic past management and storm damage), such that they are unlikely to be suitable for retention for beyond 40 years; or trees lacking the special quality necessary to merit the category A designation	Trees present in numbers, usually growing as groups or woodlands, such that they attract a higher collective rating than they might as individuals; or trees occurring as collectives but situated so as to make little visual contribution to the wider locality
Category C Trees of low quality with an estimated remaining life expectancy of at least 10 years, or young trees with a stem diameter below 150 mm	Unremarkable trees of very limited merit or such impaired condition that they do not qualify in higher categories	Trees with no material conservation or other cultural value

Project:		Cold Harbour Road Gravesend			BS 5837 2012 Trees in relation to construction - recommendations								 thelandscapepartnership landscape architecture urban design environmental planning				
Ref:		B22032															
Date:		April 2022															
Client:		Frontier Estates															
Surveyed by:		MLR															
Weather:		Cool and bright															
Tagged:		No															
Type	No.	Common Name	Height (m)	DBH (mm)	Canopy Spread				Height of branch clearance N,S,E,W	Height of crown clearance	Age class	Physiological Condition	Structural condition problems	Preliminary management	Estimated remaining contribution years	BS Category	
T	1	Fagus sylvatica (Beech)	14	750	10	7.6	6.6	6.8	2.5	1.5	M	Good	Good	None	20+	A1	
T	2	Pyrus communis (Common Pear)	6	250,230	2.5	3.5	2	2	2	2	M	Good	Good	None	20+	B3	
G	3	Ulmus procera (English Elm)	6	100	1.5	1.5	1.5	1.5	0	0	SM	Fair	Fair	Remove/coppice	<10	U	
T	4	Ulmus procera (English Elm)	5	100	1.5	1.5	1.5	1.5	0	0	SM	Dead	Poor	Fell	<10	U	
G	5	Prunus cerasifera (Cherry Plum),Sambucus nigra (Elder),Ulmus procera (English Elm)	5	100	2	2	2	2	0	0	EM	Fair	Fair	None	10+	C1	
T	6	Prunus cerasifera (Cherry Plum)	6	150	3	3	3	3	2	2	EM	Good	Good	None	20+	C2	
T	7	Laurus nobilis (Bay laurel)	4	50	1.5	1.5	1.5	1.5	0	0	SM	Good	Good	None	20+	C1	
G	8	Ligustrum ovalifolium (Common Privet)	3.5	50	1.5	1.5	1.5	1.5	0	0	M	Good	Good	None	10+	C1	
T	9	Betula pendula (Silver Birch)	12.5	175	3.5	3	1.5	2	1.8	1	EM	Good	Good	None	10+	B3	
T	10	Salix caprea (Goat Willow)	7	400	6	5.5	5	5	1	1.5	M	Good	Ivy on tree, stem not accessible	None	10+	C1	

Town and Country Planning Act 1990

Insert title of Order • GRAVESHAM BOROUGH COUNCIL (LAND SURROUNDING THE BATTLE OF BRITAIN PUBLIC HOUSE,
• NEW HOUSE LANE, NORTHFLEET)

TREE PRESERVATION ORDER, 19 94 .

Insert name of local planning authority • GRAVESHAM BOROUGH COUNCIL

Doc in this Order called "the authority", in pursuance of the powers conferred in that behalf by sections 198 and 199 ~~1990 and 1991~~ of the Town and Country Planning Act 1990, and subject to the provisions of the Forestry Acts 1967 and 1979, hereby make the following Order:—

1. In this Order:—

"the Act" means the Town and Country Planning Act 1990;

"owner" means the owner in fee simple, either in possession or who has granted a lease or tenancy of which the unexpired portion is less than three years; lessee (including a sub-lessee) or tenant in possession, the unexpired portion of whose lease or tenancy is three years or more; and a mortgagee in possession; and

Doc "the Secretary of State" means the [Secretary of State for the Environment] ~~Secretary of State for Wales~~.

2.—Subject to the provisions of this Order and to the exemptions specified in the Second Schedule hereto, no person shall, except with the consent of the authority and in accordance with the conditions, if any, imposed on such consent, cut down, top, lop, uproot, wilfully damage or wilfully destroy or cause or permit the cutting down, topping, lopping, uprooting, wilful damage or wilful destruction of any tree specified in the First Schedule hereto or comprised in a group of trees or in a woodland therein specified, the position of which trees, groups of trees and woodlands is defined in the manner indicated in the said First Schedule on the map annexed hereto[‡] which map shall, for the purpose of such definition as aforesaid, prevail where any ambiguity arises between it and the specification in the said First Schedule.

3.—An application for consent made to the authority[¶] under Article 2 of this Order shall be in writing stating the reasons for making the application, and shall by reference if necessary to a plan specify the trees to which the application relates, and the operations for the carrying out of which consent is required.

4.—(1) Where an application for consent is made to the authority under this Order, the authority may grant such consent either unconditionally, or subject to such conditions (including conditions requiring the replacement of any tree by one or more trees on the site or in the immediate vicinity thereof), as the authority may think fit, or may refuse consent:

Provided that where the application relates to any woodland specified in the First Schedule to this Order the authority shall grant consent so far as accords with the principles of good forestry, except where, in the opinion of the authority, it is necessary in the interests of amenity to maintain the special character of the woodland or the woodland character of the area, and shall not impose conditions on such consent requiring replacement or replanting.

NOTE: Where appropriate this Order has been updated to reflect statutory amendments which have resulted in the need to show substitutions or repeals of the prescribed form.

* Include only where Order contains a direction under section 201 of the Act.

‡ Map to be to a scale of not less than 25 inches to one mile (1:2500), except in the case of large woodlands when the scale shall be 6 inches to one mile (1:10000 or 1:10560).

¶ NOTE: If it is proposed to fell any of the trees included in this Order and the felling requires a licence under the Forestry Act 1967, an application should be made in the first place to the Forestry Commission.

(2) The authority shall keep a register of all applications for consent under this Order containing information as to the nature of the application, the decision of the authority thereon, any compensation awarded in consequence of such decision and any directions as to replanting of woodlands; and every such register shall be available for inspection by the public at all reasonable hours.

5.—Where the authority refuse consent under this Order or grant such consent subject to conditions they may when refusing or granting consent certify in respect of any trees for which they are so refusing or granting consent that they are satisfied—

- (a) that the refusal or condition is in the interests of good forestry; or
- (b) in the case of trees, other than trees comprised in a group of trees or in a woodland, that the trees have an outstanding or special amenity value; or
- (c) in the case of trees which are comprised in a group of trees or in a woodland, that the group of trees or the woodland, as the case may be, has an outstanding or special amenity value,

but a certificate shall not be given in the case of trees falling within (c) above if the application in respect of them has been referred by the Forestry Commissioners under section 15(1)(b) or 15(2)(a) of the Forestry Act 1967.

6.—(1) Where consent is granted under this Order to fell any part of a woodland other than consent for silvicultural thinning then unless—

- (a) such consent is granted for the purpose of enabling development to be carried out in accordance with a permission to develop land under Part III of the Act, or
- (b) the authority with the approval of the Secretary of State dispense with replanting,

the authority shall give to the owner of the land on which that part of the woodland is situated a direction in writing specifying the manner in which and the time within which he shall replant such land and where such a direction is given and the part is felled the owner shall, subject to the provision of this Order and section 204 of the Act, replant the said land in accordance with the direction.

(2) Any direction given under paragraph (1) of this Article may include requirements as to—

- (a) species;
- (b) number of trees per acre (hectare);
- (c) the erection and maintenance of fencing necessary for protection of the replanting;
- (d) the preparation of ground, draining, removal of brushwood, lop and top; and
- (e) protective measures against fire.

7.—On imposing any condition requiring the replacement of any tree under Article 4 of the Order, or on giving a direction under Article 6 of this Order with respect to the replanting of woodlands, the authority shall if such condition or direction relates to land in respect of which byelaws made by the National Rivers Authority, an internal drainage board, a water undertaker or a sewerage undertaker (as defined in the Water Act 1989) or any other authority whose functions are now exercised by the above bodies, restrict or regulate the planting of trees, notify the applicant or the owner of the land, as the case may be, of the existence of such byelaws and that any condition or direction has effect subject to the requirements of the byelaws, and the condition or direction shall have effect accordingly.

8.—The provisions set out in the Third Schedule to this Order, being provisions of Part III of the Act adapted and modified for the purposes of this Order, shall apply in relation thereto.

9.—Subject to the provisions of this Order, any person who has suffered loss or damage in consequence of any refusal (including revocation or modification) of consent under this Order or of any grant of any such consent subject to conditions, shall, if he makes a claim on the authority within the time and in the manner prescribed by this Order, be entitled to recover from the authority compensation in respect of such loss or damage:

Provided that no compensation shall be payable in respect of loss or damage suffered by reason of such refusal or grant of consent in the case of any trees the subject of a certificate in accordance with Article 5 of this Order.

10.—In assessing compensation payable under the last preceding Article account shall be taken of:

- (a) any compensation or contribution which has been paid whether to the claimant or any other person, in respect of the same trees under the terms of this or any other Tree Preservation Order under section 198 of the Act, or under the terms of any Interim Preservation Order made under section 8 of the Town and Country Planning (Interim Development) Act 1943, or any compensation which has been paid or which could have been claimed under any provision relating to the preservation of trees or protection of woodlands contained in an operative scheme under the Town and Country Planning Act 1932, and
- (b) any injurious infection to any land of the owner which would result from the felling of the trees the subject of the claim.

11.—(1) A claim for compensation under this Order shall be in writing and shall be made by serving it on the authority, such service to be effected by addressing the claim to the authority and leaving it at or sending it by post to the principal office of the authority.

(2) The time within which any such claim shall be made as aforesaid shall be a period of twelve months from the date of the decision of the authority, or of the Secretary of State, as the case may be, or where an appeal has been made to the Secretary of State against the decision of the authority, from the date of the decision of the Secretary of State on the Appeal.

12.—Any question of disputed compensation shall be determined in accordance with the provisions of section 205 of the Act.

13.—[(1) The provisions of section 201 of the Act shall apply to this Order and the Order shall take effect on 14th July 1994 .]*

~~[(2) This Order shall apply to any tree specified in the First Schedule hereto, which is to be planted as mentioned therein, as from the time when that tree is planted.]†~~ 20

NOTE: Any person contravening the provisions of this Order by cutting down, uprooting or wilfully destroying a tree, or by wilfully damaging, topping or lopping a tree in such a manner as to be likely to destroy it is guilty of an offence and liable on summary conviction to a fine not exceeding the prescribed sum[§] or twice the sum which appears to the court to be the value of the tree, whichever is the greater, or on indictment to a fine. The penalty for any other contravention of this Order is a fine not exceeding Level 4 on the standard scale[‡] on summary conviction and, in the case of a continuing offence when the contravention is continued after conviction, a person is liable on summary conviction to an additional fine not exceeding £5 for every day on which the contravention is so continued.

If a tree is removed, uprooted or destroyed in contravention of an order or, except in the case of a tree to which the Order applies as part of a woodland, is removed, uprooted or destroyed or dies at a time when its cutting down or uprooting is authorised only by section 198(6)(a) of the Town and Country Planning Act 1990 relating to trees which are dying or dead or have become dangerous, it is the duty of the owner of the land, unless on his application the local planning authority dispense with the requirement, to plant another tree of appropriate size and species at the same place as soon as he reasonably can. Except in emergency, not less than 5 days previous notice of the removal, etc., should be given to the authority to enable the latter to decide whether or not to dispense with the requirement. In respect of trees in a woodland it is sufficient to replace the trees removed, uprooted or destroyed by planting the same number of trees either on or near the land on which the trees removed, uprooted or destroyed stood or on such other land as may be agreed between the authority and the owner of the land, and (in either case) in such places as may be designated by the authority.

* This provision is not to be included unless it appears to the authority that the Order should take effect immediately.

† This provision may be included in relation to trees to be planted pursuant to a condition imposed under section 197 of the Act.

§ This sum is currently £2000 but provision is made under the Planning and Compensation Act 1991 for a fine on summary conviction not exceeding £20,000. In addition the provision for daily fines for continuing offences will be abolished. These revised penalties will become operative on the coming into effect of section 23 of that Act.

‡ £1000 but subject to alteration by Order.

FIRST SCHEDULE

TREES SPECIFIED INDIVIDUALLY*

(encircled in black on the map)

<i>No. on Map.</i>	<i>Description.</i>	<i>Situation.</i>
T1	Copper Beech (<i>Fagus Sylvatica Purpurea</i>)	Land surrounding the Battle of Britain P.H., New House Lane, Northfleet

TREES SPECIFIED BY REFERENCES TO AN AREA*

(within a dotted black line on the map)

<i>No. on Map.</i>	<i>Description</i>	<i>Situation.</i>
	NONE	

GROUPS OF TREES*

(within a broken black line on the map)

<i>No. on Map.</i>	<i>Description.</i>	<i>Situation.</i>
	NONE	

* The word "NONE" must be entered where necessary.

WOODLANDS*

(within a continuous black line on the map)

*No. on Map.**Description**Situation.*

NONE

* The word "NONE" must be entered where necessary.

SECOND SCHEDULE

This Order shall not apply so as to require the consent of the authority to

- (1) the cutting down of any tree on land which is subject to a forestry dedication covenant where
 - (a) any positive covenants on the part of the owner of the land contained in the same deed as the forestry dedication covenant and at the time of the cutting down binding on the then owner of the land are fulfilled;
 - (b) the cutting down is in accordance with a plan of operations approved by the Forestry Commission under such deed.
- (2) the cutting down of any tree which is in accordance with a plan of operations approved by the Forestry Commission under a grant scheme under section 1 of the Forestry Act 1979 except a scheme which applies to a forestry dedication covenant.
- (3) the cutting down, uprooting, topping or lopping of a tree
 - (a) by or at the request of the Post Office where the land on which the tree is situated is land which has been acquired for the purpose of the Post Office's undertaking and either works on such land cannot otherwise be carried out or the cutting down, uprooting, topping or lopping is for the purpose of securing safety in the operation of the undertaking; or the lopping in pursuance of the power conferred on any operator of a telecommunications code system by virtue of paragraph 19 of Schedule 2 to the Telecommunications Act 1984;
 - (b) by or at the request of
 - (i) a statutory undertaker or a holder of a licence under section 6(1) of the Electricity Act 1989 where the land on which the tree is situated is operational land as defined by the Act and either works on such land cannot otherwise be carried out or the cutting down, uprooting, topping or lopping is for the purpose of securing safety in the operation of the undertaking;
 - (ii) a licence holder within the meaning of Part I of the Electricity Act 1989, where such tree obstructs the construction by the licence holder of any electric line within the meaning of Part I of the said Act of 1989 or interferes or would interfere with the maintenance or working of any such line;
 - (iii) the National Rivers Authority or an internal drainage board established under the Water Act 1989, where the tree interferes or would interfere with the exercise of any of the functions of such authority or drainage board in relation to the maintenance, improvement or construction of water courses or of drainage works; or a water undertaker or sewerage undertaker appointed under section 11 of the Water Act 1989 in relation to their duties as such undertakers; or
 - (iv) the Secretary of State for Defence, the Secretary of State for Transport, the Civil Aviation Authority, or in relation to any airport managed by a company to which any property, rights or liabilities have been transferred in pursuance of a scheme made under section 1 or 15 of the Airports Act 1986, the person for the time being having the management of the airport, where in the opinion of such Secretary of State, Authority or person the tree obstructs the approach of aircraft to, or their departure from, any airport or hinders the safe and efficient use of aviation or defence technical installations;
 - (c) where immediately required for the purpose of carrying out development authorised by the planning permission granted on an application made under Part III of the Act, or deemed to have been so granted for any of the purposes of that Part;
 - (d) which is a fruit tree cultivated for fruit production growing or standing on land comprised in an orchard or garden.

THIRD SCHEDULE

Provisions of the following parts of Part III of the Town and Country Planning Act 1990 as adapted and modified to apply to this Order.

75.—(1) Without prejudice to the following provisions as to the revocation or modification of consents, any consent under the Order, including any direction as to replanting given by the authority on the granting of such consent, shall (except in so far as the consent otherwise provides), enure for the benefit of the land and of all persons for the time being interested in it.

77. **Reference of applications to the Secretary of State.**—(1) The Secretary of State may give directions to the authority requiring applications for consent under the Order to be referred to him instead of being dealt with by the authority.

(2) a direction under this section may relate either to a particular application or to applications of a class specified in the direction.

(3) Any application in respect of which a direction under this section has effect shall be referred to the Secretary of State accordingly.

(4) Where an application for consent under the Order is referred to the Secretary of State under this section, the provisions of Articles 4 and 5 of the Order shall apply as they apply to such an application which falls to be determined by the authority.

(5) Before determining an application referred to him under this section the Secretary of State shall, if either the applicant or the authority wish, give each of them an opportunity of appearing before, and being heard by, a person appointed by the Secretary of State for the purpose.

(7) The decision of the Secretary of State on any application referred to him under this section shall be final.

78. **Appeals against decisions or in default of decision.**—(1) Where an authority—

(a) refuse an application for consent under the Order or grant it subject to conditions, or

(b) give any certificate or direction, on granting consent,
the applicant may by notice appeal to the Secretary of State.

(2) A person who has made an application for consent under the Order may also appeal to the Secretary of State if the authority have neither—

(a) given notice to the applicant of their decision on the application; nor

(b) given notice to him that the application has been referred to the Secretary of State in accordance with directions given under section 77 above,

within two months from the date of receipt of the application, or within such extended period as may at any time be agreed upon in writing between the applicant and the authority.

(3) Any appeal under this section shall be made by notice in writing served within such time as is specified in subsection (4) below.

(4) The service of such a notice must be within—

(a) 28 days from the receipt of notification of the decision, certificate or direction, as the case may be, or such longer period as the Secretary of State may allow; or

(b) in the case of an appeal under subsection (2), 28 days or such longer period as the Secretary of State may allow from the end of the period of two months or, as the case may be, the extended period agreed.

(5) In relation to an appeal under subsection (2), it shall be assumed that the authority decided to refuse the application in question.

79. **Determination of appeals.**—(1) On an appeal under section 78 the Secretary of State may—

(a) allow or dismiss the appeal,

(b) reverse or vary any part of the decision of the authority (whether the appeal relates to that part of it or not), or

(c) cancel any certificate or cancel or vary any direction,

and may deal with the application as if it had been to him in the first instance.

(2) Before determining an appeal under section 78 the Secretary of State shall, if either the appellant or the authority so wish, give each of them an opportunity of appearing before and being heard by a person appointed by the Secretary of State for the purpose.

(5) The decision of the Secretary of State on such an appeal shall be final.

97. **Power to revoke or modify the consent under the Order.**—(1) If it appears to the authority that it is expedient to revoke or modify any consent under the Order granted on an application made under Article 3 of the Order, the authority may by Order revoke or modify the consent to such extent as they consider expedient.

(3) The power conferred by this section may be exercised at any time before the operations for which consent has been given have been completed.

(4) The revocation or modification of consent shall not affect so much of those operations as has been previously carried out.

98. Procedure for s.97 Orders: opposed cases.—(1) Except as provided in section 99, an Order under section 97 shall not take effect unless it is confirmed by the Secretary of State.

(2) Where an authority submit such an Order to the Secretary of State for confirmation, they shall provide the Secretary of State with a statement of their reason for making the Order and shall serve notice together with a copy of the statement on—

- (a) the owner of the land affected,
- (b) the occupier of the land affected, and
- (c) any other person who in their opinion will be affected by the Order.

(3) The notice shall specify the period within which any person on whom it is served may require the Secretary of State to give him an opportunity of appearing before, and being heard by, a person appointed by the Secretary of State for the purpose.

(4) If within that period such a person so requires, before the Secretary of State confirms the Order he shall give such an opportunity both to him and to the local planning authority.

(5) The period referred to in subsection (3) shall be 28 days from the service of the notice.

(6) The Secretary of State may confirm an Order submitted to him under this section either without modification or subject to such modifications as he considers expedient.

(7) Where a notice has been served in accordance with the provisions of subsection (2) of this section, no operations or further operations as the case may be, in pursuance of the consent granted, shall be carried out pending the decision of the Secretary of State under this section.

99. Procedure for s.97 Orders: unopposed cases.—(1) This section applies where—

- (a) the authority have made an Order under section 97 above; and
- (b) the owner and occupier of the land and all persons who in the authority's opinion will be affected by the Order have notified the authority in writing that they do not object to it.

(2) Where this section applies, instead of submitting the Order to the Secretary of State for confirmation the authority shall advertise the fact that the Order has been made and the advertisement must specify—

- (a) the period within which persons affected by the Order may give notice to the Secretary of State that they wish for an opportunity of appearing before, and being heard by, a person appointed by the Secretary of State for the purpose; and
- (b) the period at the expiration of which, if no such notice is given to the Secretary of State, the Order may take effect by virtue of this section without being confirmed by the Secretary of State.

(3) The authority shall also serve notice to the same effect on the persons mentioned in subsection (1)(b).

(4) The period referred to in subsection 2(a) must be not less than 28 days from the date the advertisement first appears.

(5) The period referred to in subsection 2(b) must be not less than 14 days from the expiration of the period referred to in subsection (2)(a).

(6) The authority shall send a copy of any advertisement published under subsection (2) to the Secretary of State not more than three days after the publication.

(7) If—

- (a) no person claiming to be affected by the Order has given notice to the Secretary of State under subsection (2)(a) within the period referred to in that subsection, and
- (b) the Secretary of State has not directed within that period that the Order be submitted to him for confirmation,

the Order shall take effect at the expiry of the period referred to in subsection 2(b) without being confirmed by the Secretary of State as required by section 98(1).

(8) This section does not apply to an Order revoking or modifying a consent granted or deemed to have been granted by the Secretary of State under Part III, Part VII or Part VIII of the Act.


GIVEN under the Common Seal of the

GRAVESHAM BOROUGH COUNCIL

the 14th day of July
on the authority of

Debra A. Givens

Authorised Sealing Officer

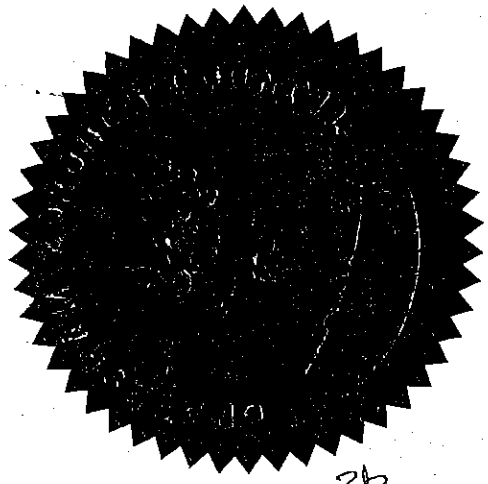

12726

Dated 14th July

19 94 .

GRAVESHAM BOROUGH COUNCIL

TOWN AND COUNTRY PLANNING ACT 1990

TREE PRESERVATION ORDER

relating to

Land surrounding the Battle of Britain P.H.,
New House Lane, Northfleet

GRAVESHAM BOROUGH COUNCIL confirm the foregoing Order
this 18th day of August 1994 on the authority of:

G. J. Chesworth


G. J. CHESWORTH
Principal Assistant Solicitor

Authorised Sealing Officer



I hereby certify that this document
is a true copy of the original

..... *R. Marden*
Secretary & Solicitor
for Gravesham Borough Council

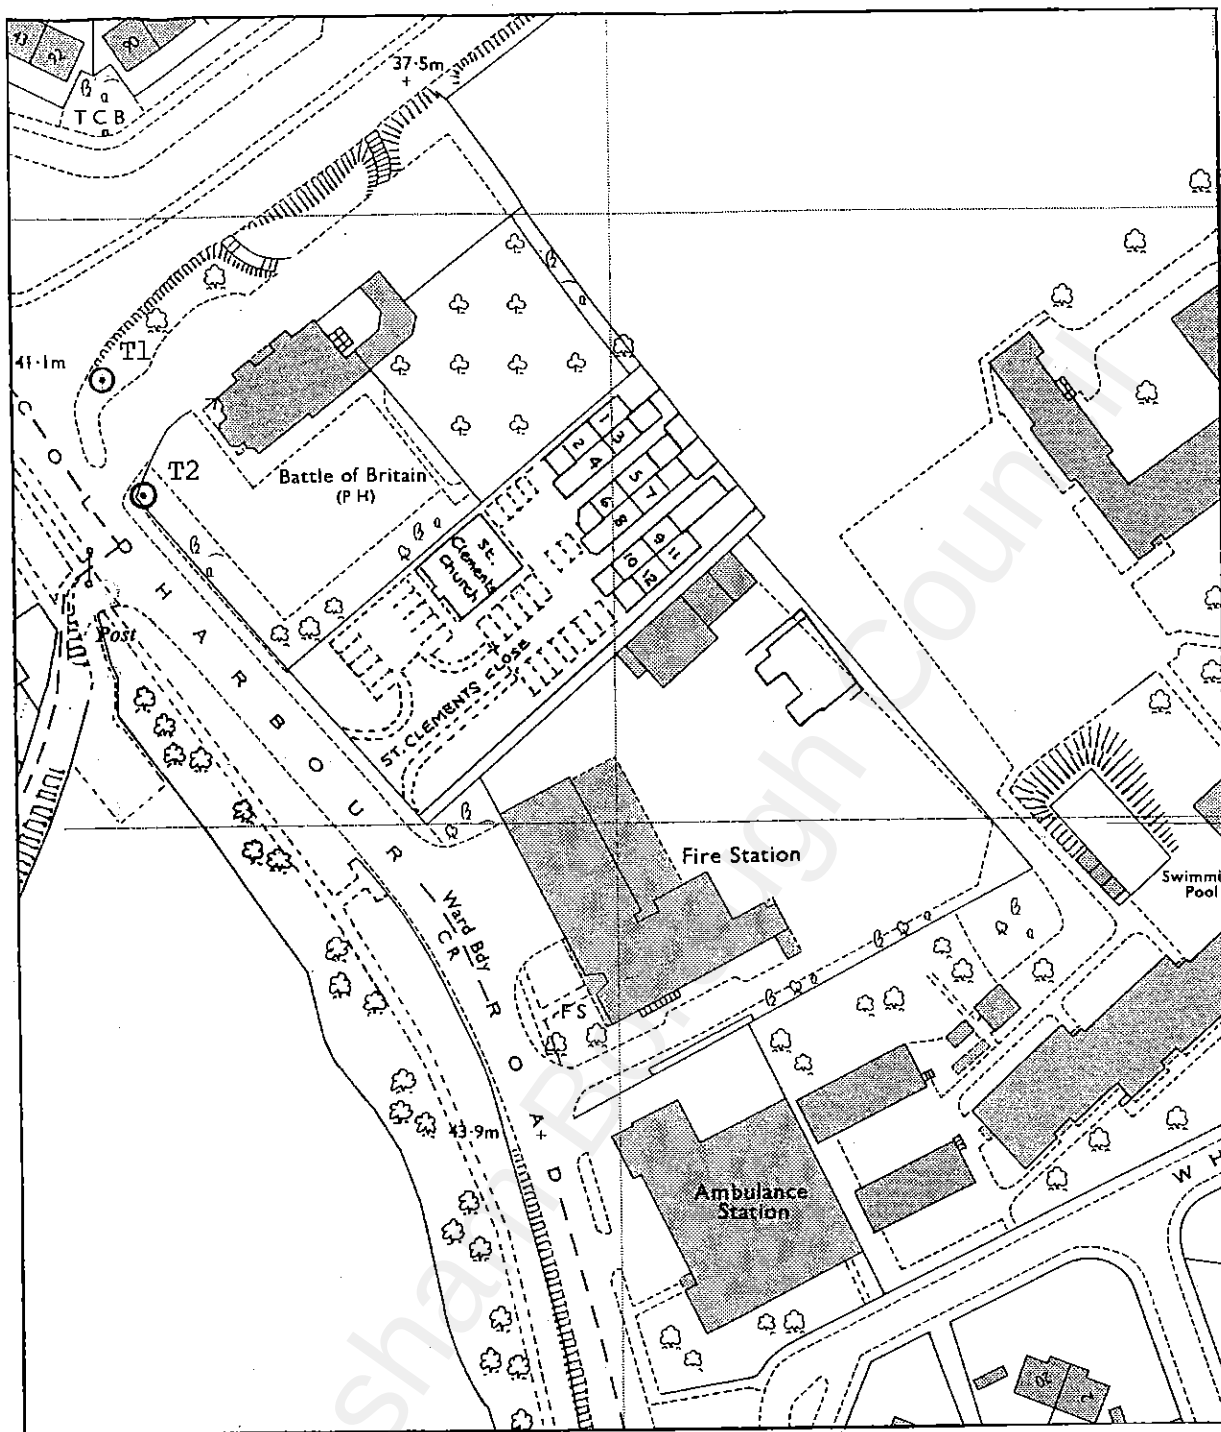

GRAVESHAM BOROUGH COUNCIL (Land surrounding the Battle Of Britain Public House, New House Lane, Northfleet, Kent) Tree Preservation Order 1994.

The Trees The Subject Of This Order :-

T1 *Tilia x europaea* (Lime)

T2 *Fagus sylvatica* 'PURPUREA' (Copper Beech)

Reference No :- PrT.187

Ordnance Survey Sheet :- TQ 6372 SE


Date 7th June 1994

Scale 1:1250

Ray Yorke BA(Hons) Dip TP MRTPI ARICS,
Borough Planning Officer,
Gravesham Borough Council,
Windmill Street,
Gravesend,
Kent.

THE USE OF CELLULAR CONFINEMENT SYSTEMS NEAR TREES: A GUIDE TO GOOD PRACTICE

GUIDANCE NOTE 12

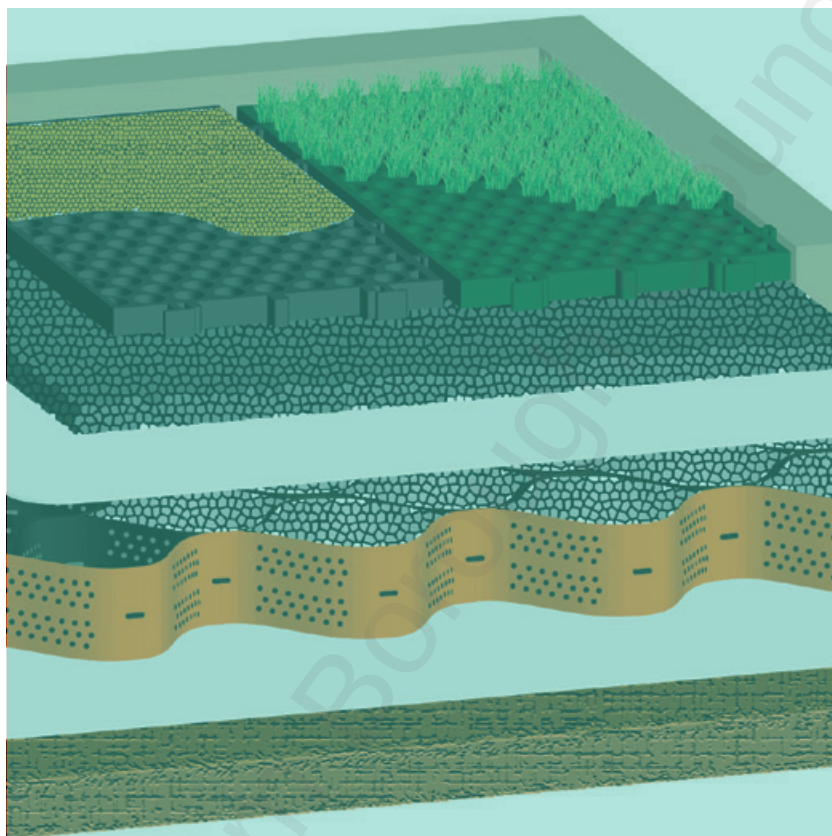

Author:
Ben Rose

Published in the UK by

Arboricultural Association,

The Malthouse, Stroud Green, Standish, Stonehouse, Gloucestershire GL10 3DL

Tel: **+44 (0)1242 522152**

Email: admin@trees.org.uk

Web: www.trees.org.uk

First published in September 2020

with the support of



Arboricultural Consultancy

ISBN 978-0-900978-65-4

© Arboricultural Association 2020

Background to the Arboricultural Association

Founded in 1964, the Arboricultural Association is the largest and longest-established UK body and authority for the amenity tree care profession. It has a base of circa 3,000 members in central and local government, commercial and educational employment, at craft, technical, supervisory, managerial, tutor and consultancy level.

The Arboricultural Association is regarded by central government departments, the Royal Horticultural Society and local government as the focal point for good practice in arboriculture, for certification and regulation of the industry, for information, education and research. It is unique in the profession in that its body of knowledge extends across the full spectrum of arboricultural issues and it can represent and advise a wide range of members from small operators to large corporate bodies, local and central government.

The Association publishes a range of technical leaflets, guidance notes and other publications concerning arboriculture, the quarterly *ARB Magazine* and the quarterly *Arboricultural Journal*. In its function as voluntary regulator for the arboricultural industry, the Association produces an online directory of Registered Consultants and Approved Contractors, all of whom have reached standards of excellence in arboriculture. The Association offers training through a varied programme of topical workshops, seminars, an annual trade show (The ARB Show) and an annual Amenity Conference. Various grades of membership exist for professional arboriculturists, those in related disciplines and enthusiasts.

Front cover image credits:

*Images courtesy of Core LP,
Advanced Arboriculture Ltd and Bosky Trees*

Image credits:

*Illustrations courtesy of Core LP and
Presto Geosystems/Greenfix.*

Photo images courtesy of

*Advanced Arboriculture Ltd, Bosky Trees
and Hauraton Ltd*

Contents

1	Using cellular confinement systems for ground protection	5
1.1	Introduction	5
1.2	The concept of cellular confinement systems	6
1.3	The relevance of different types of ground conditions	9
2	Practical application	10
2.1	Project planning	10
2.2	Suitable machinery to use for installation	12
2.3	Ground preparation	13
2.4	The use of geotextile membranes in cellular confinement systems	14
2.5	Suitable stone infill	14
2.6	Installing geocell ground protection	15
2.7	Edge supports	16
3	Suitable surface finishes	18
3.1	The need for permeable surfacing	18
3.2	Surfacing options	19
3.2.1	Porous asphalt	19
3.2.2	Loose gravel	20
3.2.3	Resin-bound gravel	20
3.2.4	Permeable block paving	21
3.3	Surface maintenance	22
4	Arboricultural implications	23
4.1	Potential impacts on tree health	23
4.2	Limitations of geocells	24
5	Key recommendations	25
	References	26

Foreword and acknowledgements

Foreword

This Guidance Note provides much needed technical direction for the arboricultural sector working alongside other professionals in development and construction.

The use of cellular confinement systems has increased over the last 20 years and the understanding of its effects and efficacy has also grown. To date, much practice regarding the installation of hard surfaces incorporating ground protection near to existing trees has been based upon an Arboricultural Practice Note (APN) 12: *Through the Trees to Development*, by Derek Patch and Ben Holding, which was published in 2007 by the Tree Advice Trust. APN 12 set out the principles of 'no dig' construction for hard surfaces, highlighting the impacts of excavation and compaction on tree roots and their soil environment.

Since then, research, technological advances and numerous studies of different materials and techniques have been explored, a revised edition of the British Standard BS5837 has been published and many architects and development and construction companies are recognising the benefits of using cellular confinement systems in this context. Indeed, as planning policy evolves it is becoming more and more relevant to consider these systems in order to meet the expected multiple demands of housing and commercial development density, while maintaining the maximum green infrastructure for societal benefit.

This Guidance Note sets out the background, concepts and relevance of cellular confinement systems, describes how to plan and prepare appropriate systems for a wide range of different applications and provides detailed technical advice and specification for implementing systems using a range of available surface treatments. It also includes detail on the arboricultural impact from the use of geocells and the limitations on their use.'

Acknowledgements

I am grateful to all of those that have reviewed and provided feedback on earlier versions of the text. In particular, I would like to express my gratitude to Dr Martin Dobson for providing detailed comments on several earlier drafts of the document. I would also like to thank Paul Muir for his thoughtful discussion which contributed to the final content and Manni Keates for producing the majority of the diagrams used in the document.

Section Using cellular confinement systems for ground protection

1

1.1 Introduction

1. Cellular confinement systems can be used for ground protection in areas where tree root damage would be caused by digging into the ground to lay a conventional sub-base for new hard surfacing and where the long-term viability of trees could be harmed if soil that they may depend upon is at risk of becoming compacted. Compaction can occur for many reasons but vehicles passing over unreinforced ground are particularly damaging, although repeated foot traffic can also be detrimental to soil structure.
2. Roots penetrate soil partly by growing through existing voids and partly by moving soil particles aside, and these processes are impeded in compacted ground where soils are dense and voids are small. The combination of high soil density and elevated soil strength can directly limit root growth. Roots and soil organisms use oxygen to convert organic compounds into energy through the process of respiration, and so they require a continual supply of oxygen from the above-ground atmosphere to be distributed through the soil profile via diffusion. The large pores in a well-structured soil are important avenues for gas exchange and they are lost when soils are compacted to high bulk densities. Soil compaction also reduces the rate of water infiltration, the availability of water to roots, and the root system's ability to support a healthy crown. The compaction of soil within tree root zones¹ can ultimately lead to crown dieback and a decline in tree health (Ruark *et al.* 1982). Once a soil has become compacted it is difficult to reverse the effects and restore a soil structure suitable for tree root growth; even with positive intervention, soil rehabilitation may take years to achieve.
3. Roads and pavements cannot be placed on an excessively yielding subgrade because if the ground moves the surface will deform or crack after a few load repetitions. To create a lasting load-supporting surface the standard engineering practice is to remove the upper layer of soil and lay a compacted sub-base that is capped by a durable wearing course. The final surface is usually engineered so that the top dressing is level with the surrounding ground. However, surfaces constructed in this way can cause severance of tree roots at shallow depth and future root growth can be inhibited by the soil compaction caused during the installation of the surface. One way to prevent damage to roots is to keep roads and paths away from trees, but with modern-day pressures to develop land it is sometimes deemed necessary to install new hard surfacing near to established trees. In such cases, where the adjacent trees are to be retained, the soil needs to be protected in some way.
4. The use of above-ground cellular confinement systems, or 'geocells', to install surfacing near trees has been employed in the UK for over 20 years. The accepted approach involves laying a geocell mat on a non-woven geotextile laid on the surface of the ground, filling it with clean stone aggregate, and topping this sub-base with a wearing course (see Figure 1). In recent years this approach has been regularly used in construction projects because it is considered to be an acceptable way of creating a new hard surface above tree root zones. But the use of geocells is not always a simple matter and the limitations of the approach are often misunderstood. Also, very few research studies have been conducted regarding the long-term effects of installing such surfaces on soil structure and on the health of adjacent trees.

¹ For the purposes of this document, tree root zones, or root protection areas, are considered to be the minimum area around a tree deemed to contain sufficient roots and rooting volume to maintain the tree's viability. The recommended methodology for calculating root protection areas is described in *BS5837:2012 Trees in relation to design, demolition and construction – Recommendations* and is generally a radial distance equivalent to 12 times the trunk diameter measured at a height of 1.5m. Greater separation distances are required for veteran trees. It is advised that a buffer zone around a veteran tree should be at least 15 times larger than the diameter of the tree or 5m from the edge of the tree's canopy if that area is larger than 15 times the tree's diameter. For ancient woodlands, the buffer zone should be at least 15m wide.

1

Section Using cellular confinement systems for ground protection

5. Guidance on installing new surfacing near trees was previously provided by Arboricultural Practice Note 12: *Through the Trees to Development* (Patch & Holding 2007). The aim of this guide is to draw on the subsequent industry experience in order to provide updated guidance that will be helpful to arboriculturists, landscape architects, engineers and building contractors.

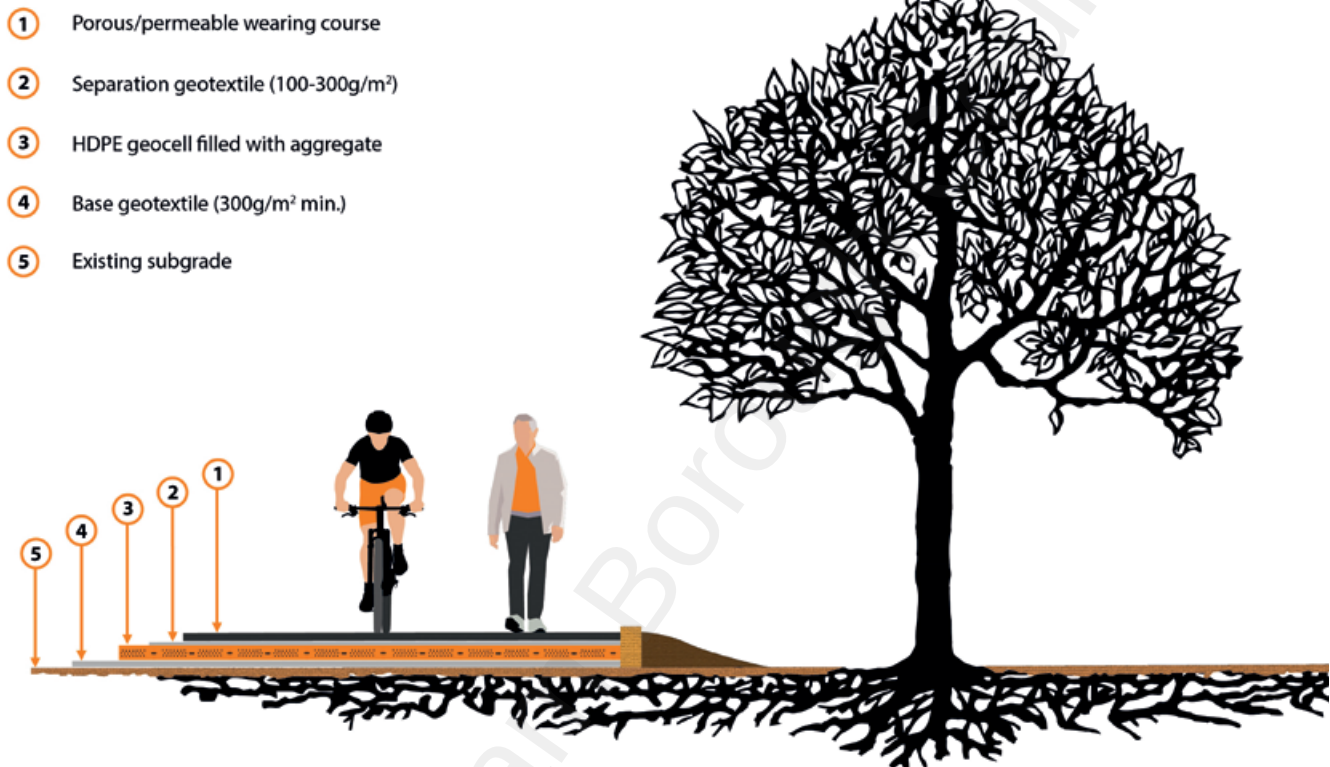


Figure 1: The basic approach to using cellular confinement systems for ground protection near trees [image courtesy of Core LP].

1.2 The concept of cellular confinement systems

6. A cellular confinement system is a series of geocells arranged in a honeycomb-like formation that is combined with an underlying geotextile and angular stone to spread loads in such a way as to minimise compaction of underlying soil. Due to its 3-dimensional structure, a geocell mat offers all-round confinement to the encapsulated material, which provides a long-term improvement in the performance of the sub-base. When a surface is reinforced in this way the load is distributed over a larger area of the subgrade-base interface, leading to lower vertical stress and reduced deformation of the subgrade (Bathurst & Jarrett 1988; Saride *et al.* 2011). Cellular confinement systems are considered to be cost effective, durable and easy to use. They also function effectively in all weather conditions (Hegde 2017). There are a variety of uses for cellular confinement systems in the construction industry, but this guidance focuses on their use when new hard surfacing is installed near trees.
7. It is relatively common for engineers to specify planar reinforcement² to improve the service life of a surface and/or to obtain equivalent performance with less depth of material. This is

Section 1

Using cellular confinement systems for ground protection

typically a 2-dimensional geogrid³ installed beneath a minimum depth of 150mm compacted stone aggregate (GMA 2000). The geogrid and the aggregate interlock and together they form a composite material that has better load-bearing properties than the aggregate alone. But this approach is not suited for use near trees because when the stone is compacted there is a high risk of compacting the soil beneath. Also, geogrids transfer loads via the 'tensioned membrane effect', and the stretching of a geogrid under tensile loading allows a degree of deformation which results in wheel rutting and the compaction of the subgrade beneath. Therefore, the use of geogrids alone is not recommended for installing new footpaths or roads near trees. They can, however, be installed beneath a geocell mat as a separation layer and to add extra strength.

8. In order to create a stable base for hard surfacing near trees it is recommended that

a cellular confinement system made of high-density polyethylene (HDPE) should be used. The plastic strips are ultrasonically bonded together to form a 3-dimensional matrix that can be filled with soil, sand, aggregate, or concrete (as shown in Figure 2), but when new hard surfacing is constructed over tree roots it is necessary to infill the geocells with angular stone because this type of fill increases friction between stones and enhances load spreading. In this context stone infill has the added benefit of being permeable, which allows water ingress and gaseous diffusion into and out of the soil.

9. The seam strength of the cells is critical to the durability of the system because these are often the weakest part of the system, and so products used should conform to ISO 13426-1:2003 Geotextiles and geotextile-related products – strength of internal structural junctions – Part 1: Geocells.
10. The walls of each cell should be textured to provide additional friction with the infill material. When geocells are infilled with stone aggregate a new composite entity is created that possesses enhanced mechanical and geotechnical properties.

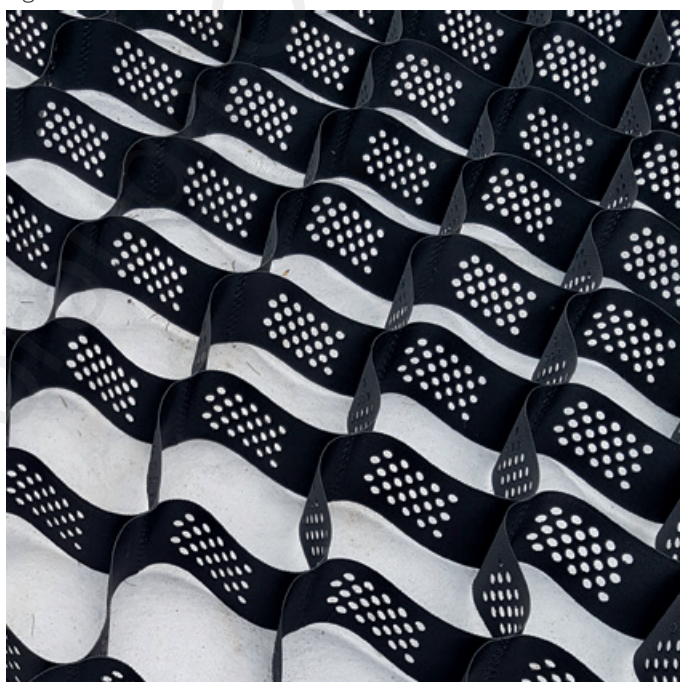


Figure 2: An expanded geocell sheet before it has been filled with stone
[Image courtesy of Bosky Trees].

² Reinforcement is a way to improve the performance or to reduce the thickness of a flexible hard surface. Hard surfaces can be reinforced using 2-dimensional or planar reinforcement, or 3-dimensional (geocell) reinforcement, or a combination of both, to improve the performance or to reduce the base layer thickness without compromising the required level of service. For this reason, these methods are commonly used to reinforce sub-bases below roads or other structures.

³ A geogrid is 2-dimensional geosynthetic material made of polypropylene or high-tenacity polyester used to reinforce soils and similar materials. Soils pull apart under tension and, compared to soil, geogrids are strong in tension. This property allows them to transfer loads to a larger area of soil than would otherwise be the case.

1

Section Using cellular confinement systems for ground protection

11. As with other geosynthetics used as surface or planar reinforcement, the development of resistance in a cellular confinement system is the result of different mechanisms working together to develop improved bearing capacity over soil. However, unlike 2-dimensional planar reinforcements which trigger the confinement and membrane effects, cellular confinement systems employ a third mechanism – the stress dispersion effect, which distributes the applied load over a wider area (Avesani Neto *et al.* 2013). The walls of the cells confine the infill material and hoop stresses prevent it from expanding laterally under load. Additional support is provided by the passive resistance of adjacent cells (as illustrated in Figure 3). A further benefit is that the downward pressure of the geocell mattress prevents the soil beneath from moving upward outside of the area directly beneath the load. All these properties work together to prevent ground deformation under load (i.e. wheel rutting). Experience has shown that harmful compaction of the soil around a tree can be avoided if an appropriate thickness of geocell is used for the loading and frequency of traverse experienced during its lifetime.

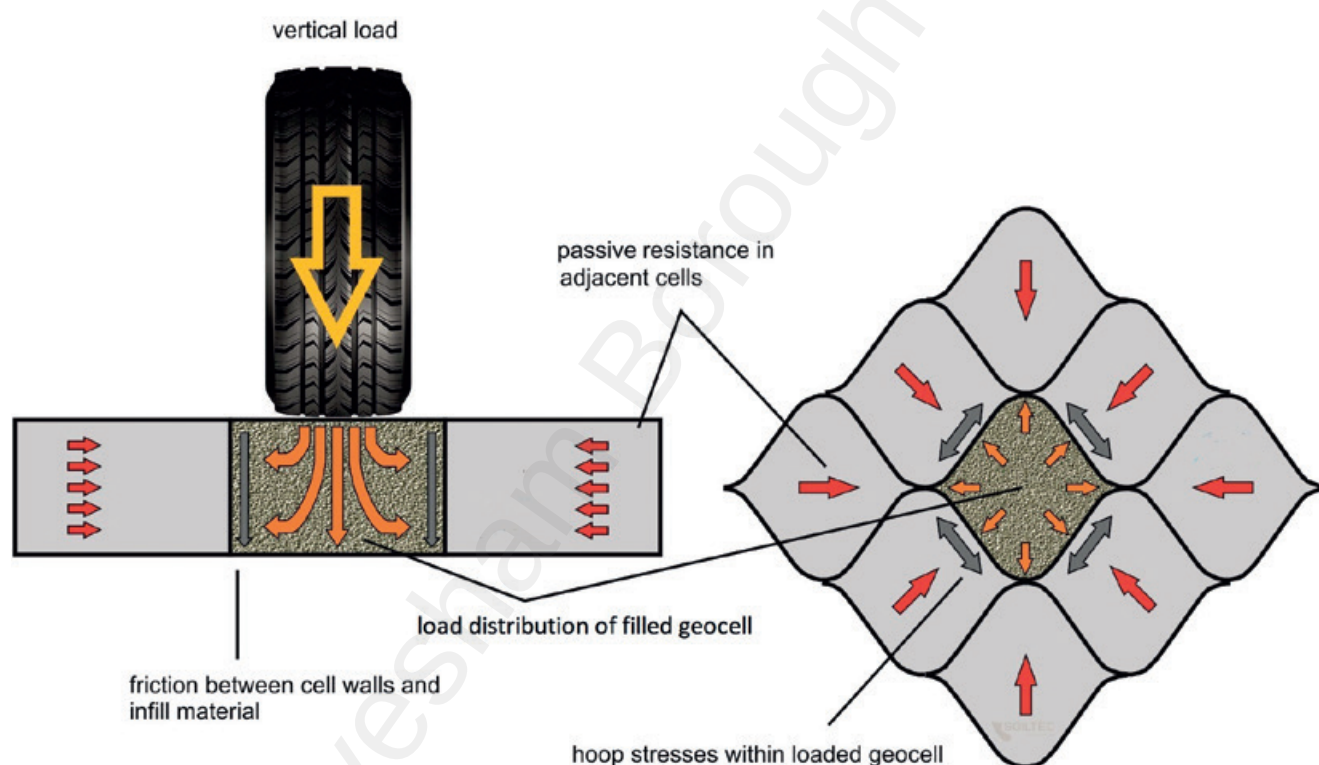


Figure 3: This diagram illustrates how forces are dispersed when a vertical load is applied to a cellular confinement system [image courtesy of Presto Geosystems/Greenfix].

12. For a cellular confinement system to function effectively it is crucial that all of the cells are fully expanded and filled to capacity. Geocells made out of flexible geotextiles are generally unsuitable for use near trees because they have a tendency to deform as they are filled with stone which impairs their dimensional stability and consequently their ability to spread the load.
13. Studies have shown that geocell foundations can provide adequate support at approximately 50% of the thickness required by non-reinforced base courses (Bathurst & Jarrett 1988). Therefore, the use of cellular confinement systems can significantly reduce the amount of material required to stabilise a soil. Sometimes this will mean that the use of a geocell sub-base is cheaper than using conventional surfacing techniques because less extensive groundworks are required and a smaller volume of new material needs to be transported to the site.

Section 1

Using cellular confinement systems for ground protection

1.3 The relevance of different types of ground conditions

14. The basic approach of using a cellular confinement system over tree root zones can be prescribed by an arboriculturist, but in order to guarantee that the surface will be suitably durable the final specification should be produced or approved by a civil engineer. This may be the project engineer or an engineer from a geocell provider (such advice is a standard service provided by most UK geocell suppliers and adds little or nothing to the cost of the installation).
15. The soil conditions need to be considered when designing a cellular confinement system because the strength of the particular soil plays an important role in the effectiveness of the geocell-reinforced base. Standard recommendations for suitable geocell depths are based on a minimum subgrade California Bearing Ratio (CBR) of 3.⁴ If the ground is soft (CBR <3) an engineer should be consulted to determine if an additional sub-base is needed beneath the cellular confinement system. It is important that the project engineer has soil information prior to the surface being specified; if a site-specific soil survey is to be carried out the key information that the engineer requires is the **saturated CBR value** of the soil.
16. In most situations the majority of a tree's fine root system is located within the upper 30cm of soil (Perry 1989; Gilman 1990), and so topsoil stripping within a tree's root zone is likely to cause harmful root damage. However, the depth and nature of the soil influence where tree roots are able to grow. In deep and well aerated soils the greatest density of roots, and almost all woody roots, will be contained in the upper 60cm of soil, although some may extend to depths of 2–3m (Dobson 1995). But in shallow or waterlogged soils roots will be located just beneath ground level, and if these roots are damaged there would be greater consequences for the tree.
17. Geocell mats need to be laid on level surfaces, so sloping or uneven ground can be challenging. The recommended approach in such situations is to first install an edge restraint (as detailed in Section 2.7), followed by the base geotextile, and then add infill to the lower areas to raise the level up to the highest point (see Figure 4). Sharp sand can be used to ramp over protruding roots but deep layers of sand beneath geocells should be avoided because there is a risk that they could be eroded by water movement which may lead to surface failures. For this reason, the use of angular stone aggregate is advised (ideally this would be the same as the infill material).

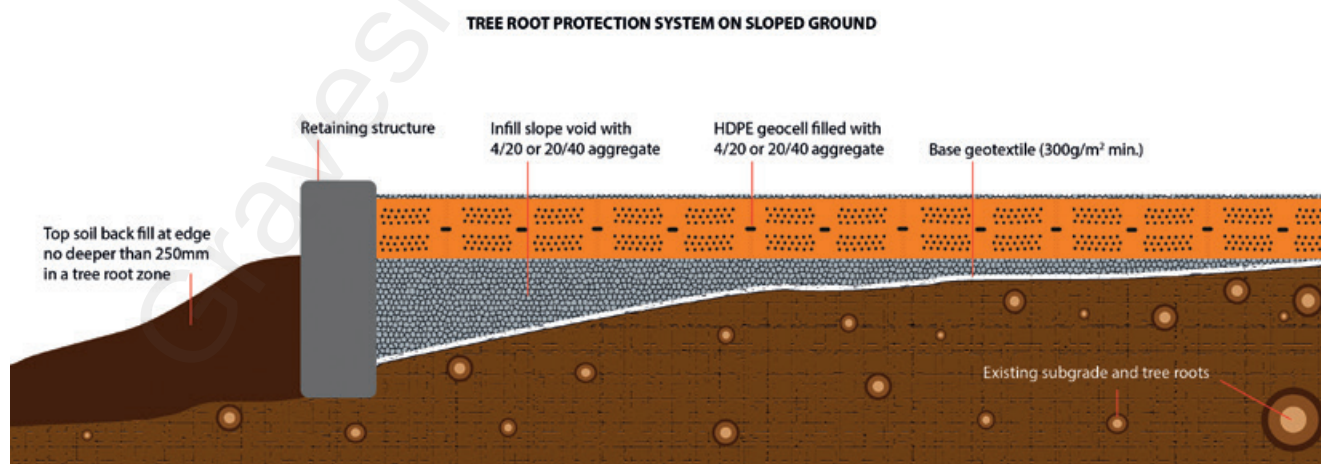


Figure 4: An example of how cellular confinement systems should be installed when the ground is sloping or uneven [image courtesy of Core LP].

⁴ It should be noted that CBR is often referred to as a number rather than a percentage, e.g. 3 rather than 3%.

2 Section

Practical application

2.1 Project planning

18. If they are to be effective, cellular confinement systems must be installed properly with due regard to the particular circumstances of the site. Practitioners must approach projects of this nature with the same degree of knowledge, care and ingenuity that they would bring to any other aspect of a construction project.
19. There are alternative construction techniques which may sometimes provide a better solution than cellular confinement systems for surfacing above tree root systems. Suitable alternatives may include piled raft solutions using conventional or screw piles, or the use of stone-filled wire gabions. All options for bridging over tree root zones should only be considered acceptable where there are discernible reasons why encroachment into the root protection areas of retained trees cannot be avoided.
20. BS5837 states that *'where permanent hard surfacing within the RPA is considered unavoidable, site-specific and specialist arboricultural and construction design advice should be sought to determine whether it is achievable without significant adverse impact on trees to be retained'*. On that basis, sufficient justification should be provided where cellular confinement systems are proposed over the root zone of trees that have been assessed to be particularly vulnerable, or those that are considered at risk of being less resilient to even a minor degree of negative impact. Also, it may be inappropriate for a cellular confinement system to be used in a root protection area when it would be one of several impacts on a tree to be retained, such that the cumulative effect might be considered to be detrimental.
21. Veteran trees are valuable and may be less resilient than trees at earlier life stages, which is why in 2012 the concept of *buffer zones* was introduced for the protection of veteran trees and ancient woodland in England (Forestry Commission & Natural England 2018). To minimise the potential for harm to veteran trees or ancient woodland it is recommended that the installation of cellular confinement systems should not be permitted within the buffer zone of an ancient woodland or a veteran tree unless it can be determined that any direct impacts to soil and roots are likely to be tolerated by the affected tree(s). A cellular confinement system could be appropriate for ground protection when temporary access is required past a veteran tree if there are no other viable options available, or as a mitigation measure if a local planning authority has decided that there are wholly exceptional reasons⁵ for surfacing to be required in a buffer zone. It should be recognised during the design process that incorporating features which encourage activity close to a veteran tree or an ancient woodland is likely to create additional pressures on the long-term management of those trees. Though not directly related to the impact of the cellular confinement system on roots and soil, a precautionary approach is recommended to ensure that the tree(s) and the species that they support would not be put at risk by any indirect impacts that may be caused by introducing the new feature.
22. When geocells are used to protect tree root zones the central concept is that they are installed *above ground* and this normally results in a surface that is around 150mm above the existing ground level for footpaths, and in excess of 300mm above for roads and driveways. In many cases the necessary level differences required for the installation of cellular confinement systems over tree root systems make the approach infeasible. Designers and their clients need to be aware of this and make sure that the necessary level differences can be accommodated within a project layout.
23. Clean angular stone is an essential component required for filling the cells, and the haulage costs of this stone can be a large proportion of the overall cost (often the proximity of quarries to the site will dictate the types of infill materials that are available). For large installations this stone is typically transported in 30-tonne heavy goods vehicles (HGVs) and so a site must

⁵ For example, infrastructure projects where the public benefit would clearly outweigh the loss or deterioration of habitat (MHCLG 2019).

Section 2

Practical application

be accessible to an HGV and must include a suitable location where the load can be tipped and stored. This is particularly important when long roads or footpaths are being installed because the delivery lorries will need to deposit the stone in a suitable location away from root protection areas. The storage area needs to have enough space for the stone and for loading-vehicles to fill the dumpers that will transport the stone to the installation site.

24. In order to protect soils near trees the geocell surface often needs to be installed at the start of the project to protect ground in advance of demolition and construction activities. Alternatively, the area where the geocells are to be installed will need to be fenced off and treated as a construction exclusion zone until the time of installation.
25. If the geocell surface needs to be used as an access road during construction, its installation should be one of the first tasks the contractor carries out. In order to do this the contractor should be informed of the root protection areas required by the trees that are to be retained (determined in accordance with the guidance provided in Section 4 of BS5837:2012). Another factor that needs to be considered is the type of traffic that the surface will be subjected to during construction because very often this is heavier than the traffic that it will experience during its intended use; vehicles of particular concern include loaded dumpers and HGVs. Geocells are suitable for temporary access routes or roadways because it is a relatively simple operation to use an excavator to carefully remove a cellular confinement system when it is no longer required.
26. In some circumstances it may be necessary to install additional protection above the geocell during the demolition/construction phase. This may be required to prevent soil compaction by heavy vehicles during the development process, or as a temporary alternative to the final wearing course which might otherwise be damaged during the work. If a temporary wearing course is not used there is also a risk that mud could sink into the stone aggregate which would reduce its long-term permeability and effectiveness in maintaining gaseous exchange with the soil.

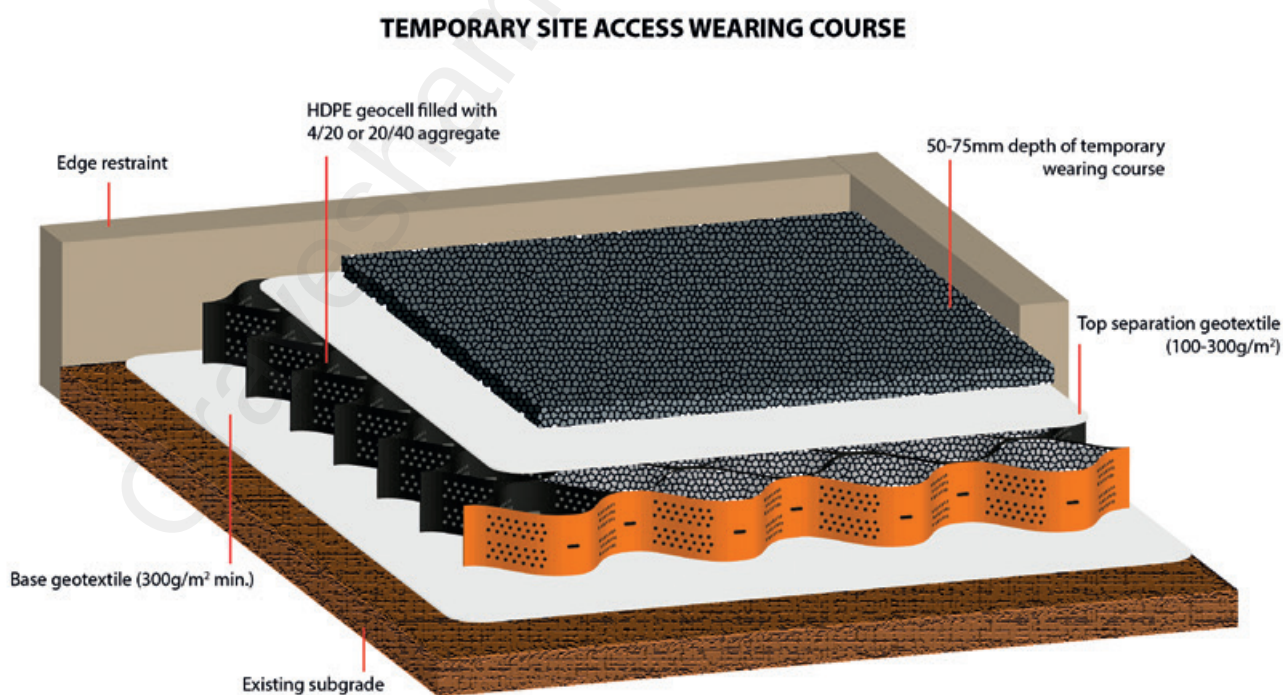


Figure 5: A geocell surface used during construction needs to be protected by a temporary wearing course and an upper geotextile is required to prevent mud from migrating down into the infill [image courtesy of Core LP].

2 Section

Practical application

In most situations overfilling the geocells with 50–75mm of material could be a suitable solution for temporary protection (as illustrated in Figure 5) but for long-term construction projects additional temporary protection would be required. Options for temporary surfacing include ply boards (for light use), heavy-duty plastic sheets, metal road plates, or a temporary sacrificial geocell layer over the surface. The latter approach is preferred as it is more likely to maintain porosity and permeability – a central concept to maintaining a healthy soil environment beneath.

27. A suitably qualified engineer should specify the appropriate depth of geocell to use for a specific location and this will depend on the bearing capacity and the strength of the soil. However, the general consensus from geocell manufacturers is that for soils with a CBR of 3 or above a loaded 6-tonne dumper can be supported by a 100mm geocell that has been overfilled by a minimum of 50mm of the same infill stone without damaging the soil structure beneath. A 150mm geocell depth is appropriate if the access road is to be used extensively by light construction traffic. However, loaded HGVs delivering construction materials, cranes, or piling rigs will require a geocell sub-base of at least 200mm.
28. The surface may also need to be protected from excessively heavy loading after construction and so vehicle use may need to be restricted; for example, bollards or barriers could be installed to prevent cars from accessing a surface that has been designed to be a cycle path only.
29. A crucial and often overlooked aspect of installing geocells is the interface between the surface laid on geocell sub-base and adjacent surfaces that have been laid on a conventional sub-base. Often the tree root zone is circular, and the intended hard surface is to cover a larger area than the sensitive root zone, and so it is tempting to only specify a geocell sub-base for the sensitive area. However, it is much easier to install surfacing in larger discrete blocks, and the final surface is likely to be much more durable if any interfaces between different surfaces are considered in the design. Therefore, it is advised that geocell is used beneath the full width of the surface rather than just part of it. The interface between different sub-bases can be incorporated within the design so that differential movement will not cause a crack to appear between the two different surface types. In order to achieve this an interface can be hidden at a point where the surfacing naturally changes (e.g. between a car-parking space and an access drive).

2.2 Suitable machinery to use for installation

30. Is not essential to use powered machinery to install geocell surfaces, and for small areas it may be easier to install them using only a shovel and a wheelbarrow.
31. Standard installations require a tracked excavator and a dumper truck. The dumper can tip stone directly into the cells and the bucket of the excavator can be used to spread the stone. The excavator should be fitted with an un-toothed spreading bucket, and on sloping ground an excavator with a tilting bucket may be more practical.
32. The ground pressure exerted by tracked excavators and loaded tracked dumpers (≤ 6 -tonne) of all sizes is generally low enough to avoid soil compaction (provided the soil is not saturated), and so they are often the most suitable machines to use when installing cellular confinement systems in root protection areas. However, tracked vehicles are not always appropriate because although they exert lower ground pressures, their skid steering can cause surface smearing which reduces gas permeability and water infiltration rates and thus causes harm to the living soil. Therefore, if a tracked vehicle needs to turn it is advised that thick plywood boards or plastic ground guards/metal sheeting are put down so that the vehicle can turn on top of them. Ground protection is more difficult to achieve when larger vehicles are employed and so they should track outside the tree's root protection area before turning.

33. Clay soils and silty clay loams are particularly prone to compaction and smearing and so vehicle use on these types of soils needs to be managed with close attention. Wet soils are also particularly susceptible to compaction and smearing because they are more pliable than drier soils. Accordingly, arboriculturists must specify that no vehicle use is permitted in root protection areas when the ground is saturated. Contractors and clients must accept that this may involve time delays but that it is necessary to minimise the impacts of installing new surfacing near established trees.

2.3 Ground preparation

34. Cellular confinement systems can be laid directly on top of lawns or other flat soil surfaces but in most cases a degree of ground preparation is required. This is often the part of the process where trees are at the greatest risk of being damaged, and so in order to minimise the risk of harming them it is advised that any ground preparation works required are carried out under the supervision of a professional arboriculturist.
35. For most projects, the removal of up to 50mm of leaf litter and surface vegetation is appropriate but if there are obvious surface roots, or if the soil layer is shallow, it may not be appropriate to remove any surface material at all. Any protruding rocks should be removed, and it is recommended that tree stumps are ground out because this causes less disturbance than digging them out. Ramps made of sharp sand should be used as a protective layer to cover up any surface roots so that they are not damaged when the infill is introduced.
36. The concept of no-dig construction was first described in Arboricultural Practice Note 1: *Driveways Close to Trees* (Patch & Dobson 1996), and the three principles set out in that guidance remain valid today:
 - Roots must not be severed.
 - Soil must not be compacted.
 - Oxygen must be able to diffuse into the soil (and carbon dioxide out of the soil) beneath the engineered surface.
37. The design should not require excavation into the soil but if there are no obvious surface roots the turf layer or any other surface vegetation may be removed. A tracked excavator with a grading bucket is normally the best machine to use to remove the turf layer because this creates an even surface. For this application excavators should be of an appropriate size for delicate works (i.e. ≤5tonne). **Ground preparation works using excavators in root protection areas must be supervised by an arboriculturist** to make sure that significant roots (single roots >25mm diameter or clusters of roots 10–25mm in diameter) are preserved and to ensure that vehicles are being used appropriately. Where there are deep soils it may be possible to remove more than 50mm from the surface, but care is essential because a large proportion of the root system is likely to be near the soil surface. Surface skimming must be stopped immediately by the supervising arboriculturist if the upper side of any significant tree roots is exposed. Even though the ground is broken by such works this approach may still be described as ‘no-dig’ in the context of installing hard surfacing near trees – the crucial distinction is that the standard practice of installing sub-surface foundations by replacing soil with compacted stone aggregate is avoided when a cellular confinement system is used.
38. With careful application a glyphosate-based systemic herbicide could be used to kill off turf in advance of laying a cellular confinement system. But in general, the application of herbicides near trees is undesirable because there is a risk that they could affect adjacent trees. However, no herbicide application is necessary prior to laying down geocells because the base geotextile and surface layers are likely to be enough to prevent vegetation growth beneath the surface.

2 Section

Practical application

2.4 The use of geotextile membranes in cellular confinement systems

39. Geotextiles are manufactured from synthetic polymers in a process that produces either a non-woven or a woven fabric. When cellular confinement systems are installed the fabric is unrolled directly on to the subgrade before the placement of the geocell mat. Its primary function is to separate the soft ground from the stone aggregate infill because when stone aggregate is placed on fine-grained soils the soil can enter the voids of the stone aggregate and impair its drainage capacity. Also, the stone aggregate can intrude into the fine soil, resulting in a reduction in the strength of the aggregate layer. For installations above tree root zones it is important that the geotextile is permeable to air and water.
40. Woven geotextiles tend to have a few openings of a relatively large size, whereas non-woven geotextiles tend to have numerous small openings and are therefore more suitable for filtration applications (CIRIA 2015). The holes in the fabric function as particle filters and in some circumstances this can prevent pollutants from reaching the soil beneath. A needle-punched non-woven geotextile is best for installing geocells near trees because it provides adequate tensile resistance and allows water to reach the subgrade (Fannin 2000).
41. Very often a second geotextile is required above the geocells to stop the bedding layer (often sand) above from mixing with the infill. The only type of surfacing that does not require a second geotextile is asphalt.
42. It is recommended that the base geotextile is made of polypropylene or polyester (min. 300g/m²) with a CBR puncture resistance of 4000N. These properties are required because the angular stone infill can puncture thinner geotextiles. The upper geotextile is required for protecting the infill matrix; this can be of the same thickness or slightly thinner (100–300g/m²). Geotextiles made from recycled products are becoming increasingly available and they can be used in cellular confinement systems if they have sufficient tensile strength and puncture resistance.
43. Sometimes a 'cake' can form on the upper side of a filtration geotextile and because of this there will always be a concern that the geotextile will clog and become less permeable. It must be accepted that any geotextile will partially clog because some soil particles will embed themselves on or in the geotextile fabric. However, there is a lot of data suggesting that permeable surfaces are very robust and in most cases do not completely seal (DCLG 2009). The aim should be to avoid situations where the geotextile will clog to the degree where the system will be insufficiently permeable to gas and water. This is the primary reason that the infill used should not contain fine-grained material. It is worth considering the risk of sediment migration when designing the cellular confinement system, to ensure that stormwater does not carry too much material downhill onto the permeable surface. It follows that a cellular confinement system with a permeable surface course should not be installed at the low point of a site's surface drainage.

2.5 Suitable stone infill

44. Angular stone binds through interlocking, and in cellular confinement systems this cohesion is aided by the texture of the geocell walls. If the stone is not angular it does not lock within the geocells and the surface will deform in use. Marine-dredged shingle and river gravel are therefore unsuitable infill materials because they have rounded edges.
45. For cellular confinement systems above tree root zones, given the size of the geocells and the interlock required, the infill should ideally be crushed 20/40 stone (this means stones that are between 20mm and 40mm in diameter). However, where this is not available 4/20 stone can be used. In all situations the infill material should be washed or graded so that it contains no fine particles (fines).

46. The aggregate must have enough internal strength to perform both during installation and in the long-term. Preferably the infill will be a crushed hard rock. However, due to haulage costs, the availability of infill will be dictated by the site location and the material produced at local quarries. Some parts of the UK do not naturally contain suitable stone for infilling cellular confinement systems and so it would need to be imported from elsewhere. Crushed granite, basalt or limestone are ideal. Flint is less suitable because some rounded edges remain after it has been crushed and the shiny faces of the fractured stone are slippery. When geocells are used for tree protection, MOT Type 1, Type 2 and Type 3 are not suitable for use as infill because they contain fines.
47. Generally, the amount of infill required can be calculated using the following equations:

Quantity of 4/20 stone infill required = m² of coverage × depth of geocells (m) × 2 tonnes

Quantity of 20/40 stone infill required = m² of coverage × depth of geocells (m) × 1.8 tonnes

48. An aggregate cover on top of the geocells does not contribute towards the increase of the bearing capacity of the surface but it protects the geocells, and so it is advised that geocells are overfilled by a minimum of 25mm additional aggregate before the surface layers are installed above.

2.6 Installing geocell ground protection

49. A base geotextile is always required beneath a cellular confinement system to separate the fill material and the subgrade; this geotextile must cover the entire area to be surfaced. If several sheets are required they should overlap by at least 30cm. On top of that the geocell mat is stretched out and staked in place. J-hooks (steel reinforcing bars bent into a 'candy cane' shape) are the easiest type of stake to use, but construction pins or wooden stakes can also be used. Ideally the length of the stake should be at least three times the cell height.
50. If conditions require that adjacent sections of the geocell be joined together rather than butted against each other, zip ties or staples can be used. Staples through each set of adjoining cells are attached using a heavy-duty stapler (usually available from the geocell supplier) and surplus cells can be cut off using a Stanley knife with a hooked blade. The infill material is then poured into the open pockets of the geocell.
51. Where possible, vehicle use should be restricted to areas outside the tree root zones. When introducing the stone the excavator should be positioned outside of the root protection area or on top of a stone-filled geocell mat. In some situations it may be possible to fill the geocells from the side of the track furthest away from the trees without any vehicles entering the root protection areas. When tracked vehicles are used in root protection areas, installers should start at one end of the area to be surfaced and work progressively past the tree(s) so that the need for manoeuvring is reduced, but if this is not possible additional ground protection may be required (as described in Section 2.2).
52. Engineers and contractors who are unfamiliar with cellular confinement systems will instinctively want to compact the infill but this is inappropriate when installing cellular confinement systems near trees because it would result in the compaction of the soil beneath the geocells and defeat the purpose of using the system. It is recommended that settlement of the infill material is achieved by a minimum of four passes of a smooth roller (max. weight of 1000kg/m width without vibration), or alternatively by several passes with a tracked excavator. After several passes the infill reorients and becomes stable, causing local fill stiffening. The aim is to reach the point where the infill is consolidated. Checks should be made to ensure that the infill is fully consolidated before laying the wearing course.

2 Section

Practical application

2.7 Edge supports

53. Edging is not required for the stability of the cellular confinement system but it is necessary to retain the wearing course and the filling of incomplete cells at the edge of a surface. Block paving that does not have a fixed edge can shift and the joints can spread, leading to movement and potential migration of the bedding material beneath. Asphalt can also crack at the edge if it is not properly retained. In all cases the appearance of the surface is adversely affected, and the longevity of the surfacing is greatly reduced. For these reasons all projects that include the use of cellular confinement systems should include a detailed specification for surface edging.
54. Kerb stones set in concrete haunchings dug into the ground are typical edging for standard surfaces but often this method of installation is not suitable where the kerblines passes through a tree root zone because the necessary excavations are likely to result in damaged roots. There are a variety of suitable alternative solutions including fixed sleepers, peg-and-board edging, concrete kerbs set above ground and pinned metal or plastic edging. Suitable systems are described in Table 1.

Table 1: The types of edging available for retaining wearing courses.

	Peg-and-board edging The use of treated timber peg-and-board edging is often the simplest option. However, loading can be high when the surface course is laid and so pegs are required at 1m spacing to prevent the side boards from bowing. A drawback of this approach is that the wood can splinter if tracked vehicles drive over it. Also, the wood deteriorates over time and so it is not a suitable solution for projects that are intended to have long life spans. Thicker tanalised boards can be used for longer-term installations. The wide boards typically provide a more attractive finish and they last a lot longer than thinner boards.
	King-posts Where deeper above-ground support is needed steel I-bars can be used to support large wooden sleepers. A drawback of this approach is that the I-bars need to be set in concrete, and that part of the process could damage roots if it is not carried out with due care [image courtesy of Advanced Arboriculture Ltd].

Section 2

Practical application



Standard kerbs set on top of concrete-filled geocells

If the levels suit, standard kerbstones can be set on top of the geocells. The edge cells can be filled with concrete and the haunchings are above the cellular confinement system. The finish can look very good when this has been carried out properly.



Small concrete kerbs pegged and set in concrete

Where only small load resistance is required narrow concrete kerbstones can be set in concrete at the edge of the geocells, and these can be further stabilised by wooden pegs. This creates an attractive finish that is comparable to standard surface installations.



Railway sleepers fixed in place

An advantage of using railway sleepers is that they are easy to source and quick to install. They are particularly good for temporary access roads because they can be easily removed at the end of the project and re-used.



Metal or plastic edging strips

There is a range of edging products that are designed to retain block paving or to provide a clean edge to landscape areas. These are typically L-shaped edging strips that are secured by being pinned into the ground below [image courtesy of Hauraton Ltd].

3

Section

Suitable surface finishes

3.1 The need for permeable surfacing

55. Permeable paving needs to be suitable for pedestrian or vehicular traffic and contain pathways that allow air and water to pass through. Although some permeable paving materials are nearly indistinguishable from non-permeable materials in construction and appearance, their environmental effects are qualitatively different because they allow gases, water and heat to be exchanged between the soil and the atmosphere.
56. In the UK, sustainable drainage systems (SuDS) are actively encouraged in new development schemes. Cellular confinement systems topped with a permeable surface can be part of a SuDS design because they allow water to infiltrate directly into the soil and contribute to managing stormwater by detaining runoff, increasing infiltration, and treating water quality (Ferguson 2005).
57. If a permeable surface is acting as a road surface it may need to be adopted by the local highway/roads authority or drainage approval body. This is a complex subject, and guidance on relevant approval or adoption protocols may need to be sought from local stakeholders before a detailed design is drawn up.
58. In most cases standard tarmac surfacing is inappropriate above tree root zones because it seals the surface of the soil, preventing the ingress of water and gaseous exchange between the soil and the atmosphere. If this is a concern, alternative pathways for air and water to reach the soil beneath can be designed. Still, there may be exceptional circumstances where an above-ground geocell sub-base with a sealed surface is the only way of avoiding a standard foundation that would cause direct damage to tree roots. In order to decide if an impermeable surface is a suitable solution the arboriculturist will need to assess the overall impact of such works by considering the health of the affected trees, the proportion of the root zone affected, and whether the soil structure and water supply will be sufficient to fulfil the physiological needs of the tree in the long-term.

3.2 Surfacing options

3.2.1 Porous asphalt

59. Porous asphalt is an open-graded aggregate bound with asphalt cement to produce a permeable surface that allows water and air to pass through. It is probably the best surface to use over cellular confinement systems because it tends not to have cracking or pothole formation problems. Also, it provides a neat finish that looks very similar to standard tarmac. The asphalt binder never really hardens and so it interacts with the geocell base to form a single flexible structure. The installation of porous asphalt is marginally more expensive than standard tarmac but it has benefits for adjacent trees, pollution control, site drainage and stormwater management.
60. An advantage of porous asphalt is that it does not require proprietary ingredients to be manufactured. Most asphalt providers can easily prepare the mix, and since installing it does not require unusual equipment or specialised paving skills, general paving contractors can install it as they would standard surfaces. The asphalt must be thoroughly mixed immediately before being laid or there can be an uneven distribution of binder as the surface is laid, and this leads to some parts of the surface being impervious because they have too much binder in the pores and other areas breaking up because there is too little binder around the aggregate. Standard porous asphalt may be used for cyclepaths and footpaths but stronger binding agents are required for car parking areas and driveways because the power steering of modern vehicles can cause the surface aggregate to break up.

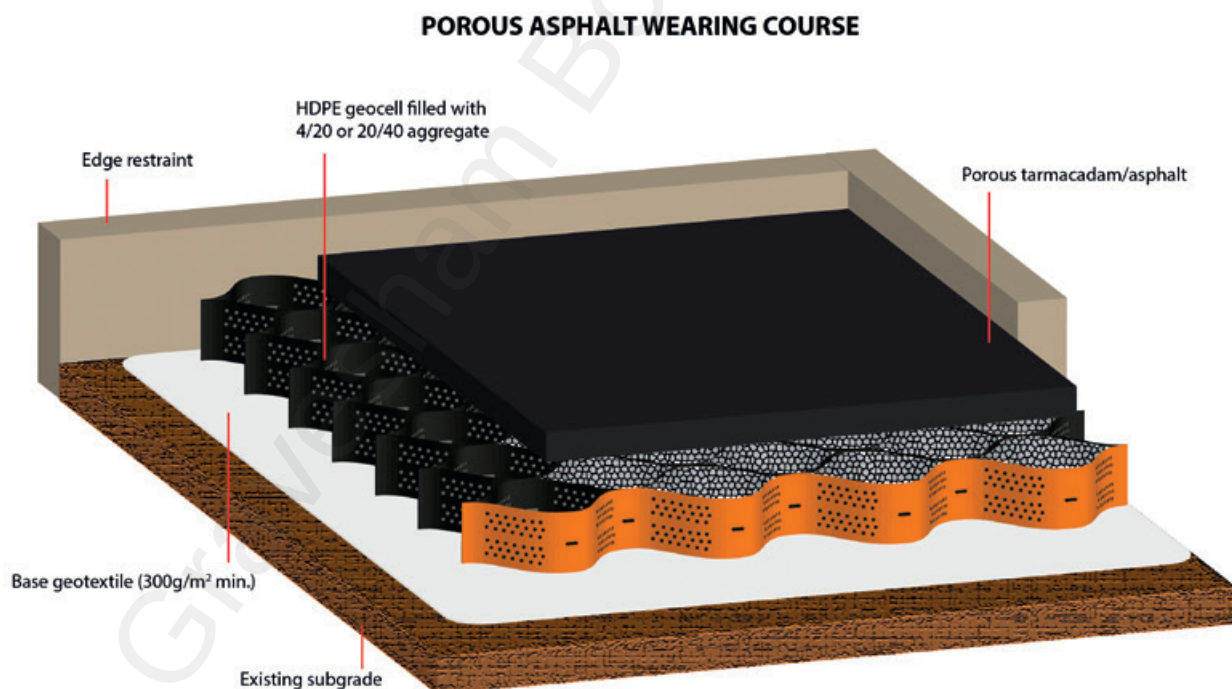


Figure 6: The typical composition of a porous asphalt surface with a geocell sub-base [image courtesy of Core LP].

3

Section

Suitable surface finishes

3.2.2 Loose gravel

61. Residential driveways typically bear light and slow-moving vehicular traffic and unbound gravel is suitable for this type of use. It can also be used as a temporary surface, but the gravel is often disturbed by vehicles turning, and there is a risk of the upper separation geotextile tearing and the gravel contaminating the infill. Also, as with all gravel installations, the surface camber must be suitable or the gravel will migrate downhill.
62. Small plastic stabilisation grids are the best solution for car parking areas. They are not a solution in themselves beneath trees because they do not spread loads sufficiently to prevent soil compaction and they also need to be laid on a sub-base. However, they can be used to retain gravel or soil above a geocell sub-base (see Figure 7). One particular benefit of these small panels is that they are lightweight and easy to put into position. Another advantage is that they can easily be removed and replaced if necessary.
63. Stabilisation grids with grass are possible over tree root systems but their appearance suffers under heavy traffic. For this reason, permeable grass-covered surfacing is best for overflow parking areas or other areas that have only occasional use.

STABILISATION GRID WEARING COURSE FILLED WITH SOIL OR GRAVEL

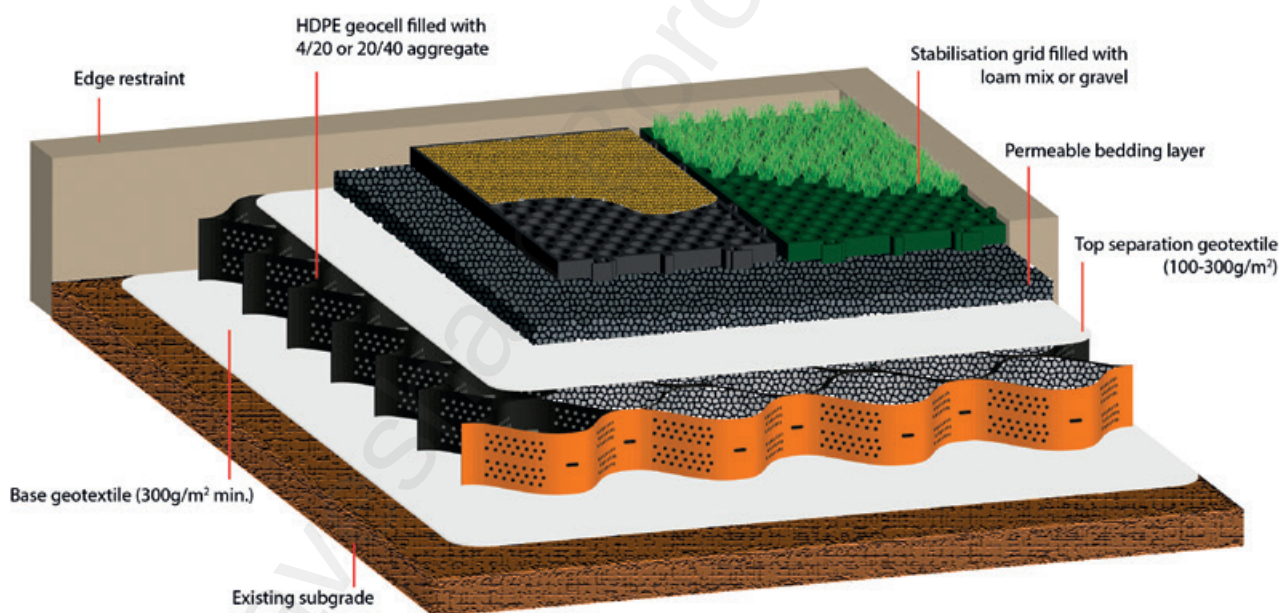


Figure 7: The sub-base configuration required for gravel or grass surfacing [image courtesy of Core LP].

3.2.3 Resin-bound gravel

64. Resin-bound gravel provides a permeable and durable wearing course. It is better than loose gravel when a surface has heavy traffic because it remains stable. The resin is typically UV-stable polyurethane, mixed with aggregate with a typical grading of 6–10mm. A variety of resin-bound products are available, and they come in a range of colours. Specifiers should be aware that resin-bonded surfaces are typically thin layers (18–25mm) and they have to be laid on a porous asphalt base (80–150mm deep).

3.2.4 Permeable block paving

65. Block paving (concrete block permeable paving, porous block paving, and clay block permeable paving) can be used as a wearing course. It is commonly used because the final surface is attractive. It is highly permeable and can bear heavy traffic. Another benefit is that this is a surface that most contractors know how to install.
66. Joint fill material is spread into the joints and the surface is vibrated to settle the blocks, bedding and joint-fill into a firm position. Block paving is a sensible solution on corners or on sloping ground because the surface is given stability by the interlocking blocks. The adjacent blocks wedge together and so creep is resisted when they are put under horizontal loads such as vehicle braking or turning.
67. Paving blocks need to be laid on a bed of sand or fine stone chippings and so a second geotextile is required above the infill to prevent the sand from migrating down the profile. There are numerous different types of block paving available and paving experts should be consulted to find the best type for specific applications.

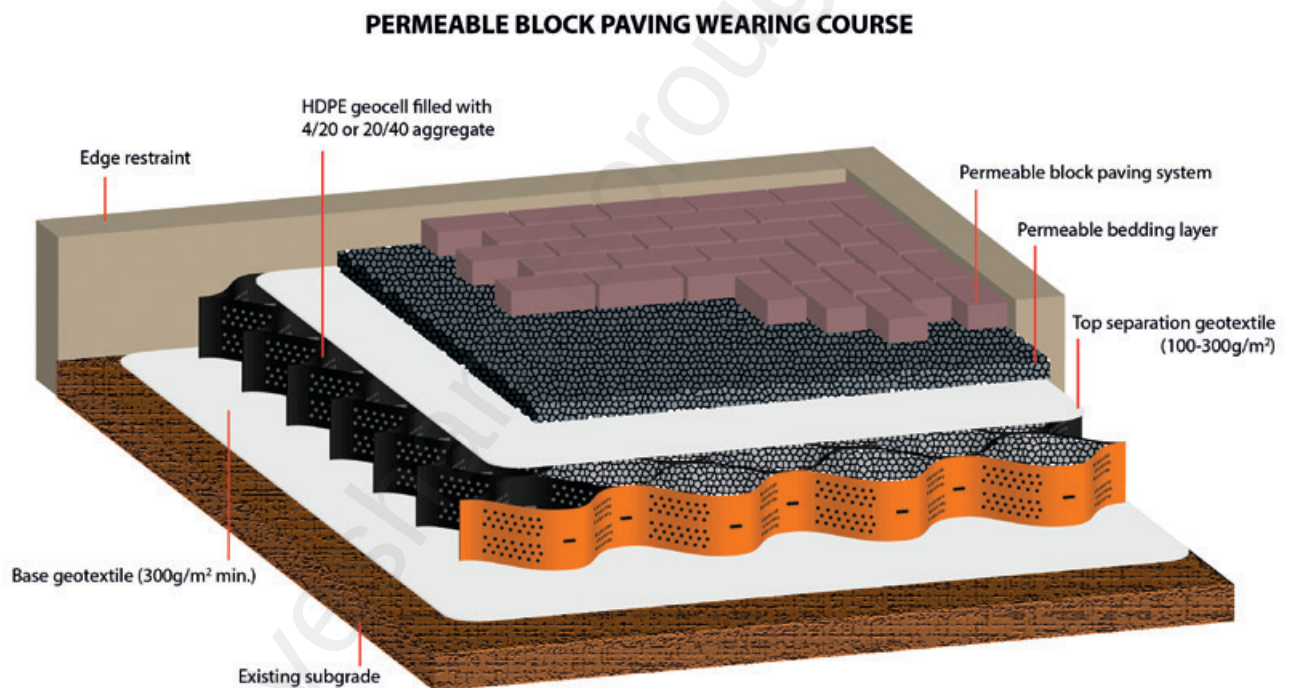


Figure 8: The recommended specification when installing permeable block paving above a cellular confinement system
[image courtesy of Core LP].

3

Section

Suitable surface finishes

3.3 Surface maintenance

68. Over time all permeable surfaces are likely to require a degree of maintenance to prevent them from becoming clogged because this would impair their function and could therefore adversely impact adjacent trees. Smaller particles trap larger particles. Therefore, the rate of clogging increases as more fines are trapped. It is a good idea to install permanent signs to alert maintenance personnel to keep silt and debris away from a porous surface; and also to warn them not to seal the pavement or use de-icing salts if there are adjacent trees.
69. Surface clogging can be managed by regular maintenance. Brush and suction road sweepers should be used for regular cleaning of roads and car parks. Leaf and litter vacuums are a quick and effective way to clean porous surfaces; these are small machines that are pushed by the operator. Hand-held pressure washers can also be used to unblock surface pores that have become blocked with moss, tree leaves and needles. All types of cleaning are most effective when they are done before clogging is complete.
70. As a general rule, permeable surfaces should be cleaned once every year to remove silt and dirt particles. Surfaces beneath trees that drop lots of blossom or fruit may need to be cleaned more regularly (refer to Section 20.14 of the CIRIA SuDS Manual for more detailed maintenance guidance).
71. The HDPE that makes up the cells can degrade if exposed to sunlight and the cells can also be damaged by traffic if they protrude. Consequently, the functionality of the system is impaired and the surface develops a tatty appearance. Therefore, uncapped cellular confinement systems need to be checked annually and topped up with suitable stone if any cells are visibly exposed.

4.1 Potential impacts on tree health

72. A major concern about surfacing above a tree root zone is the impact that this will have on the availability of water and oxygen to the soil immediately beneath the surface. Soil aeration deficiencies result in reduced levels of tree root growth (Weltecke & Gaertig 2012) and so it is important that new surfacing above a tree root system maintains gas permeability at the soil-atmosphere interface.
73. Laying a new load-bearing surface over an area of ground is likely to increase the bulk density of the soil beneath to some degree. As a result, the soil will contain less macropore space and the pores will have fewer connections between them. With these effects on the soil profile, wide or extensive surfacing above a root zone will have the effect of decreasing the saturated hydraulic conductivity and increasing the tortuosity⁶ of flow paths through the soil. With reduced levels of oxygen and water there will also be reduced biological activity in the soil, which will consequently decrease the opportunities for soil-pore creation and the turnover of soil organic matter. An inadequate supply of oxygen impairs root growth and function because respiration becomes anaerobic, which is inefficient and does not release enough energy to maintain essential physiological processes in root tissue (Roberts *et al.* 2006). Consequently, the uptake of water and nutrients by the root system decreases, causing reduced photosynthesis above ground. It has been found that low soil oxygen concentrations increase the susceptibility of plants to diseases, the virulence of pathogens, or both (Craul 1992). These adverse effects would be more extreme beneath an impermeable surface because air and rainwater would be prevented from infiltrating directly from the above-ground atmosphere.
74. There is a risk that the preparatory works required to level the ground could cause direct root damage which would leave affected trees vulnerable to soil-borne pathogens and, ultimately, this could lead to the accelerated decline of the tree.
75. Taking into consideration the effects that surfacing has on soil structure and permeability, it cannot be said that any form of hard surfacing will have no impact on the environment of tree roots growing beneath. When the full implications of installing cellular confinement systems are considered, one has to conclude that the impact of installing such a surface will inevitably have a small adverse impact on the health of affected trees. But experience has shown that healthy trees usually remain in good health when a permeable hard surface is laid on top of a geocell sub-base within their root zones. Overall, it seems that in a great majority of cases the impact of installing cellular confinement systems in tree root zones is small enough for it not to result in an obvious deterioration in the condition of affected trees, and the benefits of using this approach far outweigh the problems of laying a conventional surface.
76. BS5837:2012 recommends that new permanent hard surfacing should not exceed 20% of any existing unsurfaced ground within the root protection area of a tree (BSI 2012). This is a cautious recommendation and it should not necessarily be considered an absolute limit because in some circumstances covering a higher proportion of the root zone with a permeable surface may be acceptable, provided that it has been sufficiently justified.

⁶ Tortuosity is one of the properties of a porous material, usually defined as the ratio of actual flow path length to the straight distance between the ends of the flow path. In terms of void connectivity, a highly tortuous soil is the opposite of an uncompacted and biologically active loam soil. If the soil's pore passages are tortuous (as in a compacted soil), gaseous diffusion and soil water movement are inhibited.

4

Section

Arboricultural implications

4.2 Limitations of geocells

77. Underground services should not be routed beneath cellular confinement systems because they may need to be accessed in the future, either for repair or for making new connections, which could severely compromise the installation. On many development sites this can be a significant limitation. Therefore, when cellular confinement systems are specified the requirement for new underground services, and where they need to be installed, must be detailed at the planning stage.
78. Ramping up from an existing road to a new geocell surface can be difficult to achieve if there are tree roots at the edge of the road. It may be necessary to create a build-out in the road so that the ramp can be installed before the geocell begins. The preference would always be to have ramping formed outside tree root zones but the level change caused by building a new surface above ground often means that it is not practically feasible to ramp up from existing roads. In such situations some dig (and possibly ground consolidation) within the root protection zone of adjacent trees would be required in order to smoothly connect the two different types of surface construction. Alternatively, a metal ramp can be installed on mini-piles. Adjacent trees could be compromised if there are significant roots where the excavation for a ramp is required, and all parties involved should be aware that in this context the use of a cellular confinement system may not be an appropriate solution. The level differences caused by installing above-ground surfacing can have a variety of consequences; for example in some cases they will dictate the floor level of buildings in the vicinity.
79. HDPE geocells are made of virgin plastic and, provided they are not exposed to sunlight, they have a design life of 120 years. They can also be reused. The design life of permeable paving is approximately 20 years (DCLG 2009; CIRIA 2015). Therefore, in most cases the wearing course or edging would need to be replaced before the cellular confinement system.
80. The static load of the infill is low (approx. 15–20kPa per metre height depending what infill is used), and geocell mats disperse active loads. Therefore, unless the ground is particularly soft (CBR < 3), the stone-filled geocell sub-base can be up to 2m deep and used by refuse trucks or fire engines without causing compaction of the soil beneath.
81. There are few long-term studies that demonstrate the effectiveness of cellular confinement systems near trees. At present it is difficult to say with confidence what the long-term impacts of such surfacing may be on the soil beneath. Independent studies that measure the bulk density, moisture and oxygen levels of soils beneath geocells would help develop understanding of how effectively they function. Also, key features of cellular confinement systems, such as the effects of infill materials, stress distribution patterns, joint strength and wall deformation characteristics, have still not been fully explored. Refined guidance should be developed as the use of cellular confinement systems increases and if data from long-term tree health monitoring studies become publicly available.

5 Key recommendations

- 1) The use of cellular confinement systems can be effective in protecting soils and tree root systems when new hard surfacing is required near trees. However, in this context the installation of geocell sub-bases inevitably involves working on top of tree root systems and as such there will be an elevated risk of damaging tree roots and the structure of the soil. Therefore, careful working procedures are required to ensure that trees are suitably protected when the installation works are carried out.
- 2) The installation of cellular confinement systems should be directed by a project-specific arboricultural method statement. The arboricultural method statement should list any aspect of the proposed construction project that has the potential to adversely impact adjacent trees and detail appropriate methodologies for how the works will be undertaken in ways that would minimise those impacts.
- 3) Tree roots can be directly damaged as the ground is levelled in advance of laying down a cellular confinement system and so it is recommended that this part of the process is carried out under arboricultural supervision. The use of a tracked excavator within a tree's root protection area should only be permitted if it is supervised by a suitably qualified arboriculturist. Local authorities should condition such supervision and stipulate that records of the supervision visits be provided to demonstrate that the works have been carried out appropriately.
- 4) The cellular confinement system must be filled with clean angular stone that contains no fine material. To protect the geocell membrane it is advised that geocells are overfilled by a minimum of 25mm. In order to function effectively it is crucial that all of the cells are fully expanded and filled to capacity. Therefore, if there is insufficient space for a cell to be expanded it should be cut away and discarded.
- 5) When cellular confinement systems are installed within tree root zones it is important that the wearing course is permeable so that air and water can reach the soil beneath. Systems should be put in place to ensure that the surface is regularly cleaned so that it maintains its porosity.
- 6) The means to successfully prevent ground compaction during construction need to be planned from the conceptual stages of a building project. It may be that the no-dig surface needs to be installed and used during construction, and in other situations the ground may need to be protected until it is time to install the cellular confinement system. Therefore, the project arboriculturist needs to work with the architect, the project engineer, and the building contractor during the planning stages as well as during the construction of the surface.

References

- Avesani Neto, J.O., Bueno, B.S. and Futai, M.M. (2013). A bearing capacity calculation method for soil reinforced with a geocell. *Geosynthetics International*, Vol. 20(3):129–142.
- Bathurst, R. and Jarrett, P.M. (1988). *Large-Scale Model Tests of Geocomposite Mattresses over Peat Subgrades*. Transportation Research Record Journal of the Transportation Research Board.
- BSI (2012). BS5837:2012 *Trees in relation to design, demolition and construction – Recommendations*. British Standards Institution, London.
- CIRIA (2015). *CIRIA 753: The SuDS Manual*. CIRIA. London.
- Craul, P.J. (1992). *Urban Soil in Landscape Design*. John Wiley & Sons Inc.
- DCLG (2009). *Understanding Permeable and Impermeable Surfaces – Technical Report on Surfacing Options and Cost Benefit Analysis*. Department of Communities and Local Government. London.
- Dobson, M.C. (1995). Tree Root Systems. *Arboriculture Research and Information Note 130/95/ARB*. Arboricultural Advisory and Information Service. Farnham, Surrey.
- Fannin, J. (2000). *Basic Geosynthetics: A Guide to Best Practices in Forest Engineering*. Ph.D., P. Eng., Forest Resources Management and Civil Engineering, University of British Columbia, Canada.
- Ferguson, K. (2005). *Porous Pavements*. CRC Press, Florida.
- Forestry Commission and Natural England (2018). *Ancient Woodland, Ancient Trees and Veteran Trees: Protecting them from Development*. Available at: www.gov.uk/guidance/ancient-woodland-and-veteran-trees-protection-surveys-licences
- Gilman, E.F. (1990). Tree root growth and development. 1. Form, spread, depth and periodicity. *Journal of Environmental Horticulture*, Vol.8: 215–220.
- GMA (2000). *Geosynthetic Reinforcement of the Aggregate Base/Subbase Courses of Pavement Structures – GMA White Paper II*; by Berg, R. B., Christopher, B. R. and Perkins, S.; prepared for American Association of Highway and Transportation Officials Committee 4E, Geosynthetics Materials Association, Roseville.
- Hegde, A. (2017). Geocell reinforced foundation beds – past findings, present trends and future prospects: A state-of-the-art review. *Construction and Building Materials*, Vol. 154: 658–674.
- Jackson, R.B., Canadell, J., Ehleringer, J.R., Mooney, H.A., Sala, O.E. and Schulze, E.D. (1996). A global analysis of root distributions for terrestrial biomes. *Oecologia*, Vol. 108: 389–411.
- MHCLG (2019). *National Planning Policy Framework: Conserving and enhancing the natural environment*. Available at: www.gov.uk/government/publications/national-planning-policy-framework--2
- Patch, D. and Dobson, M. (1996). *Driveways Close to Trees*. Arboricultural Practice Note 1. Arboricultural Advisory and Information Service. Alice Holt Lodge, Surrey.
- Patch, D. and Holding, B. (2007). *Through the Trees to Development*. Arboricultural Practice Note 12. Arboricultural Advisory and Information Service. Alice Holt Lodge, Surrey.
- Perry, T.O. (1989). Tree roots: facts and fallacies. *Arnoldia*, Vol. 49, 1–21.
- Roberts, J., Jackson, N. and Smith, M. (2006). *Tree Roots in the Built Environment*. DCLG, TSO, London.
- Ruark, G.A., Madler, D.L. and Tattar, T.A. (1982). The influence of soil compaction and aeration on the root growth and vigour of trees – a literature review. Part 1. *Arboricultural Journal*, Vol. 6(4), 251–265.
- Saride, S., Sitharam, T.G. and Puppala, A.J. (2011). The function of basal geogrids in minimizing rutting of geocell reinforced subgrades. *ASCE Geofrontiers*, 4645–4652.
- Weltecke, K. and Gaertig, T. (2012). Influence of soil aeration on rooting and growth of the Beuys-trees in Kassel, Germany. *Urban Forestry & Urban Greening*. Vol. 11, 329–338.

Gravesham Borough Council

Gravesham Borough Council

Arboricultural Association

The Malthouse, Stroud Green, Standish, Stonehouse, Gloucestershire GL10 3DL

☎ 01242 522152 ✉ admin@trees.org.uk www.trees.org.uk

ISBN 978-0-900978-65-4

Printed September 2020


© Arboricultural Association 2020




Tree Survey

Key


Tree categories




Category A tree
BS5837 2012



Category B tree
BS5837 2012



Category C tree
BS5837 2012



Category U tree
BS5837 2012

Root protection area (RPA)

Diameter of trunk

Tree number as recorded on Survey Schedule

Tree canopy

Coloured symbol indicating BS category as shown left

G OR G


Group (Group of similar trees recorded together in schedule). Colours same as BS5837 2012 categories for trees (left)

H

Hedge Colours same as BS5837 2012 categories for trees (left)

The above BS categories are judgements of quality and value based on the contribution each tree would be expected to make over a given period of time, categories A, B and C being high, moderate and low respectively. Category U represents trees that, in their current context, should be removed for sound arboricultural reasons. For exact definition of BS categories refer to notes accompanying schedule.

Note: Underlined tree number denotes tree located by eye. Locations should be checked on site and if necessary drawings amended.

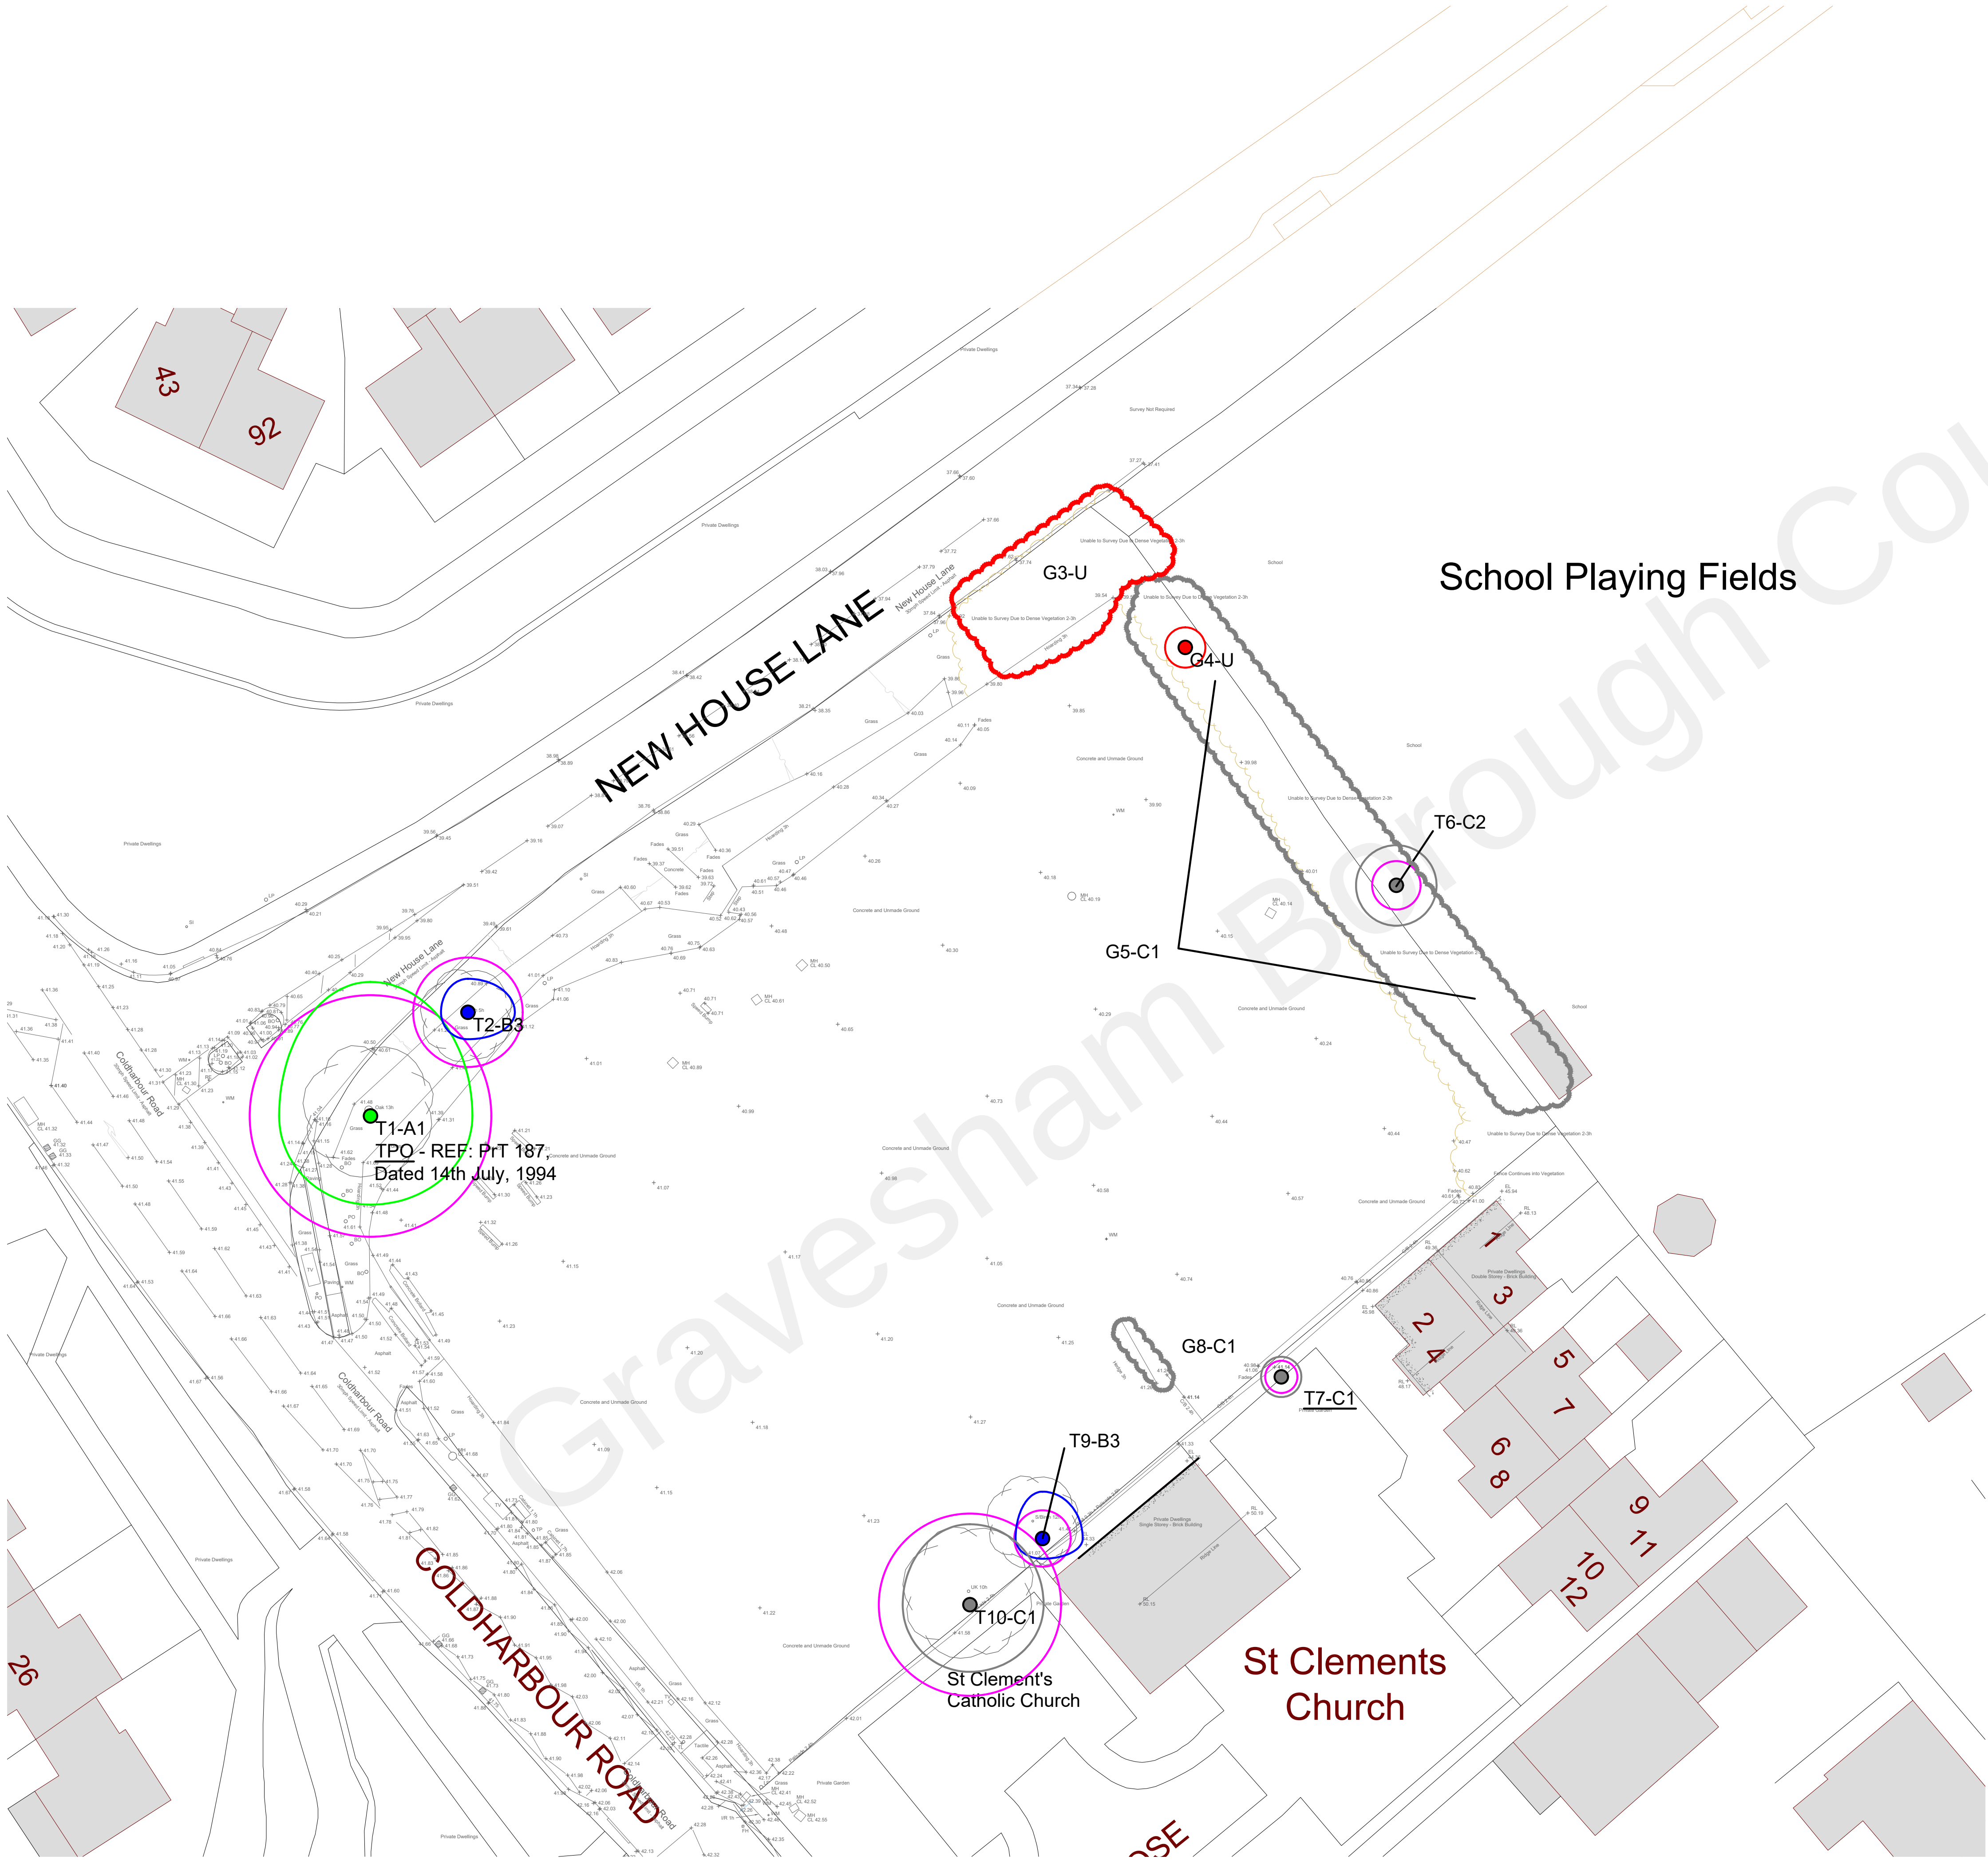

TPO information added	B	OT	31/08/2022
Scale updated	A	OT	23/08/2022
Revision	Number	By	Date




Project
Coldharbour Road, Gravesend

Drawing
Tree Survey


Status
PLANNING

Do not scale off drawing. All dimensions & Levels are to be checked on site. Any discrepancies must be reported to the landscape architect immediately.
Copyright THE LANDSCAPE PARTNERSHIP LTD

Bedford	01234 261315	☐
Woodbridge	01394 380509	☒
London	020 3092 4141	☐
Norwich	01603 230777	☐
Job No.	B22032	
Dwg. No.	601B	
Scale	1:250@A1	
Drawn	IO	
Checked	MLR	
Date	19-04-2022	



Key

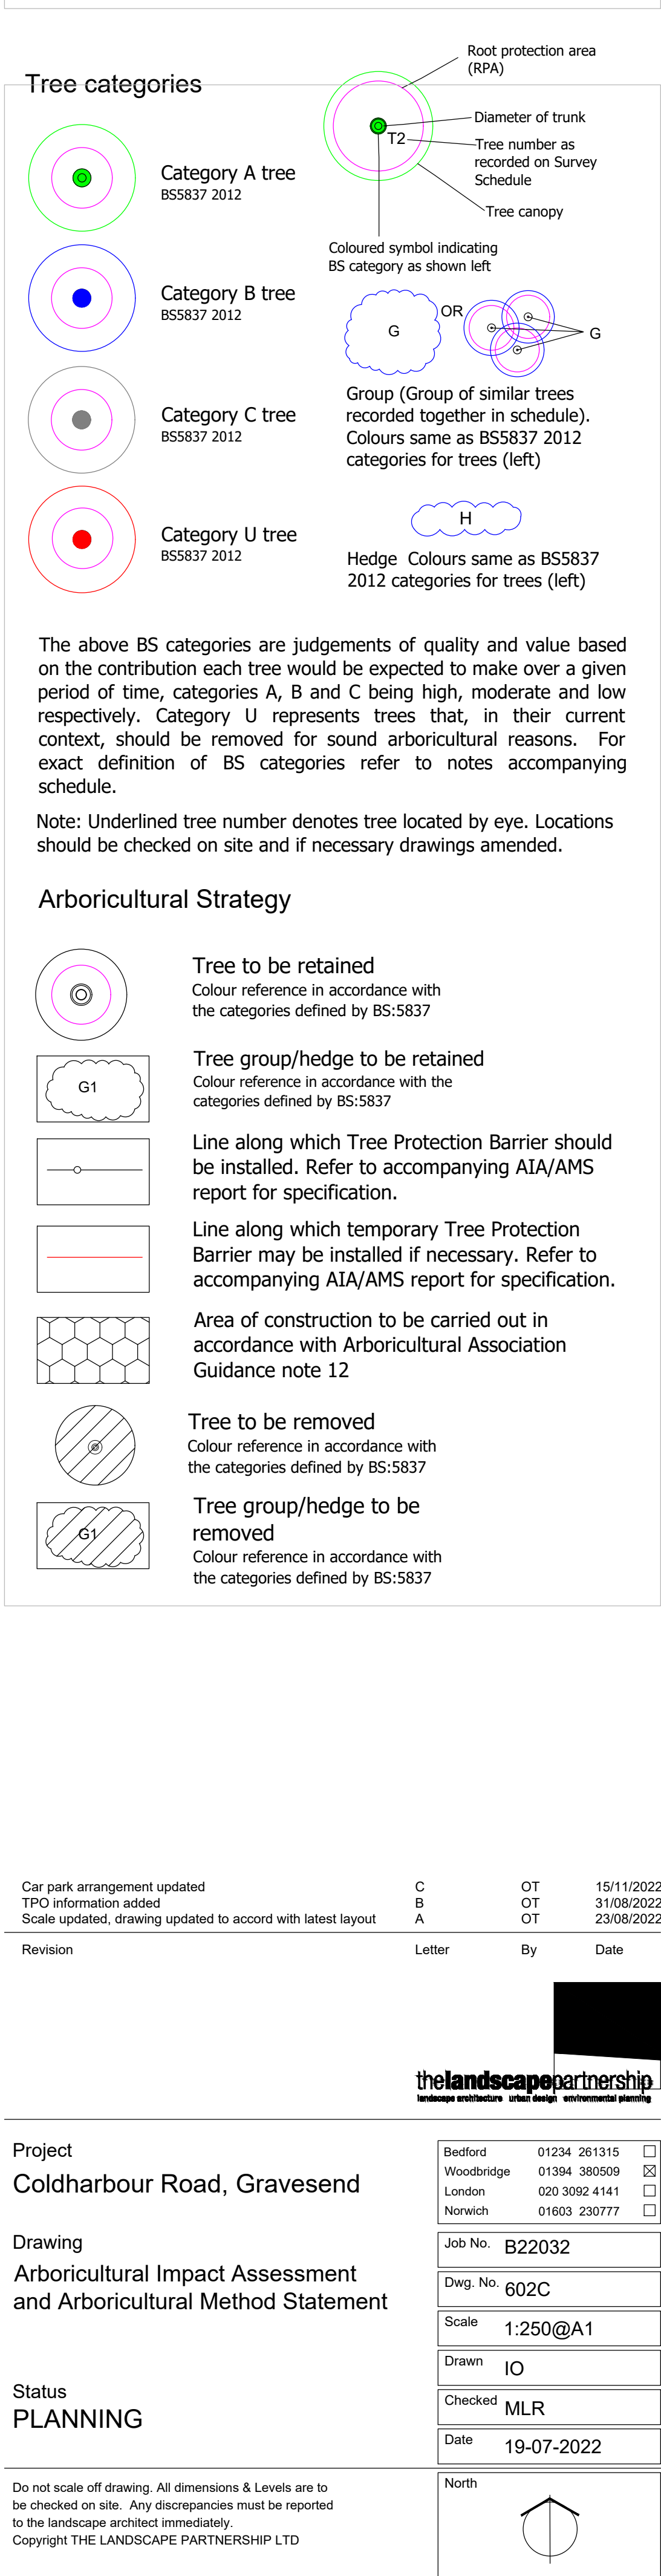

Note: Underlined tree number denotes tree located by eye. Locations should be checked on site and if necessary drawings amended.

Tree to be retained
Colour reference in accordance with the categories defined by BS:5837

Tree group/hedge to be retained
Colour reference in accordance with the categories defined by BS:5837

Line along which Tree Protection Barrier should be installed. Refer to accompanying AIA/AMS report for specification.

Line along which temporary Tree Protection Barrier may be installed if necessary. Refer to accompanying AIA/AMS report for specification.

Area of construction to be carried out in accordance with Arboricultural Association Guidance note 12

Tree to be removed
Colour reference in accordance with the categories defined by BS:5837

Tree group/hedge to be removed
Colour reference in accordance with the categories defined by BS:5837



thelandscapepartnership
landscape architecture urban design environmental planning

Bedford	01234 261315	☐
Woodbridge	01394 380509	☒
London	020 3092 4141	☐
Norwich	01603 230777	☐

Drawn	IO
Checked	MLR
Date	19-07-2022

North

